




GAP Full Plan


Shorter pedestrian crossings


Separated vehicle movement


Enhanced plaza space

Bicycle connections

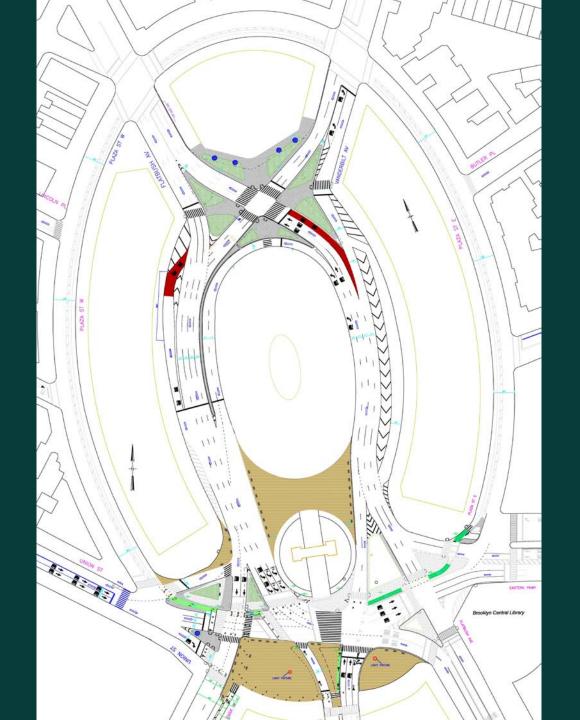


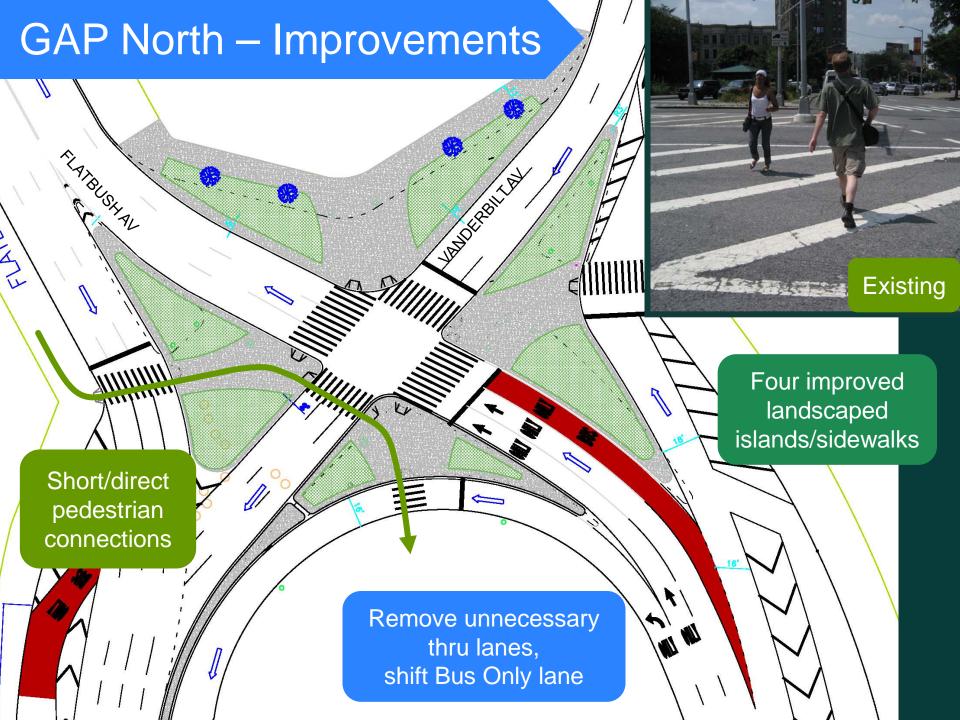

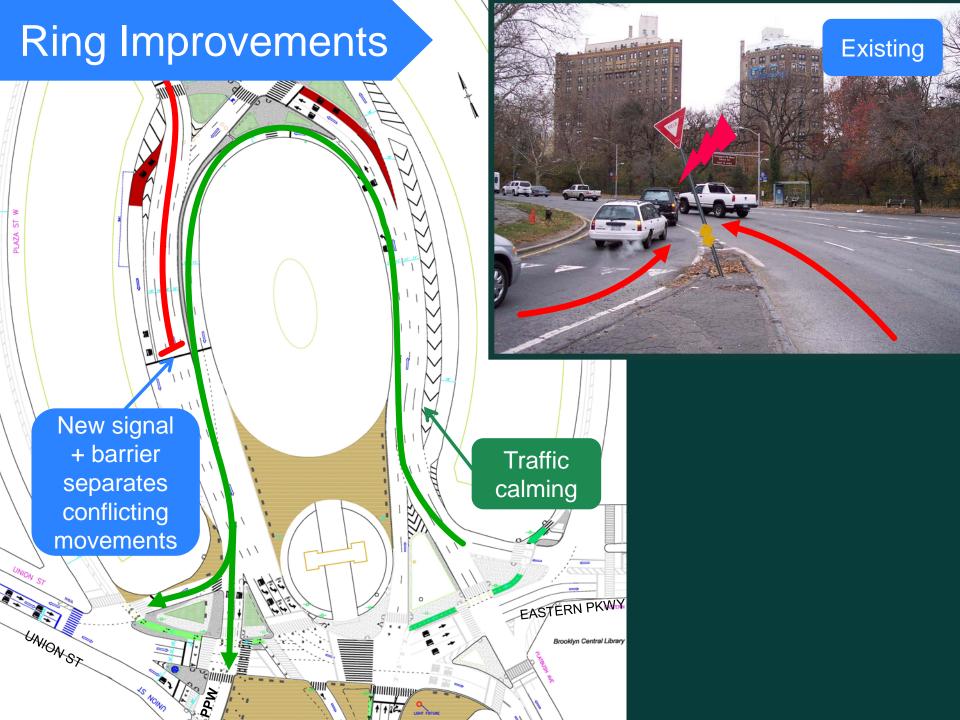

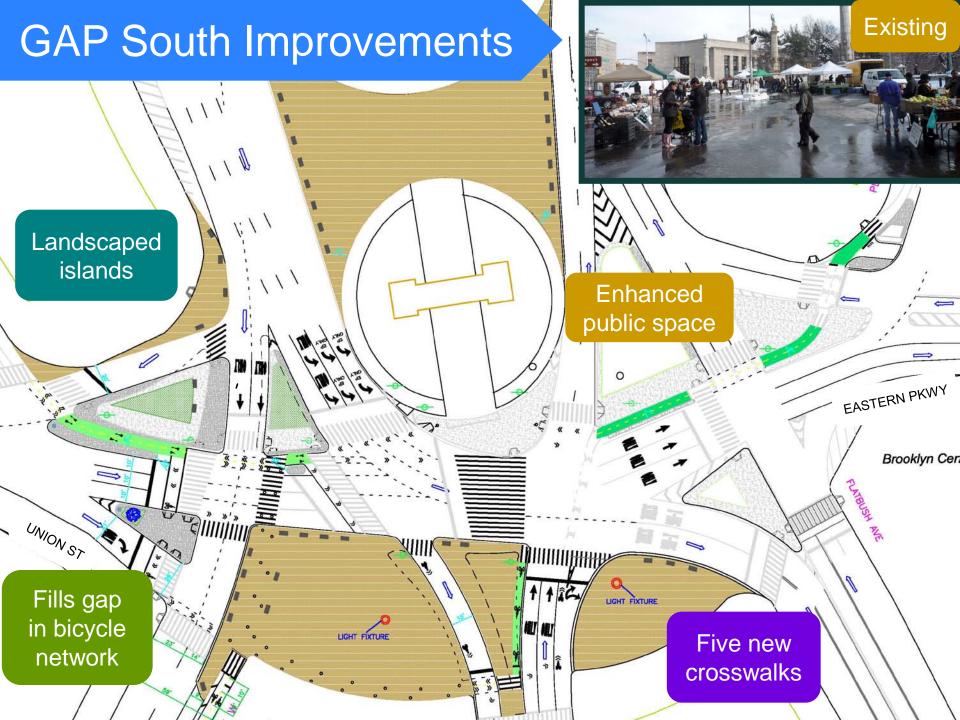

Implementation Schedule

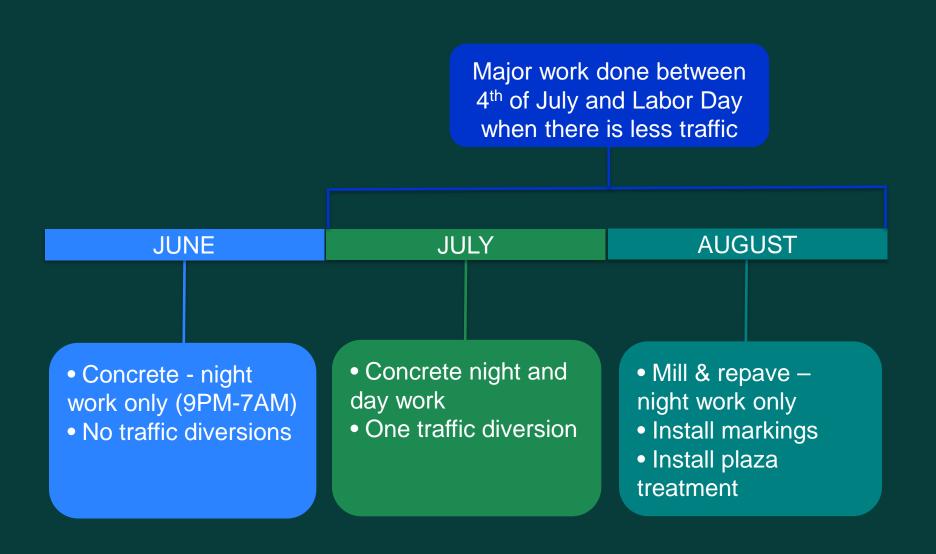


June



Concrete Islands


- All night work
- Islands 1 & 2 start simultaneously
- Islands 3 & 4 started as 1 & 2 are completed

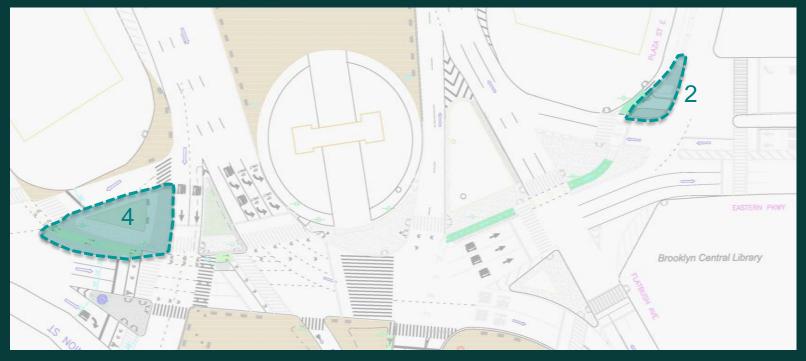


July

Concrete Islands

- Day crew added for island 5
- Night crews continue on all islands

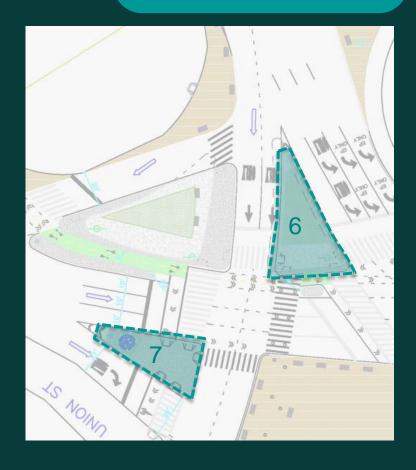

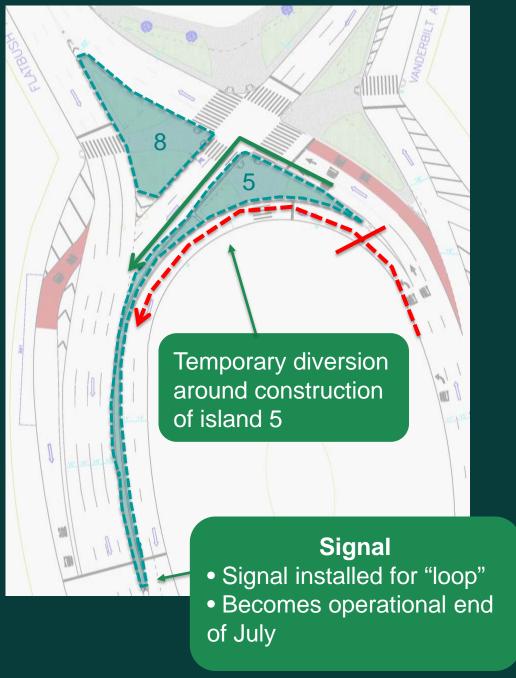

August **Repave Roads** Night work only **Install Plaza Treatment** Crushed gravel **Install New** surfacing **Markings** •Granite blocks

