

East River Waterfront Esplanade

CB 3 Parks Committee Update

October 13, 2016




Agenda

- Recap
- Work Update
- Timeline
- Q&A

East River Waterfront Esplanade

Project Site

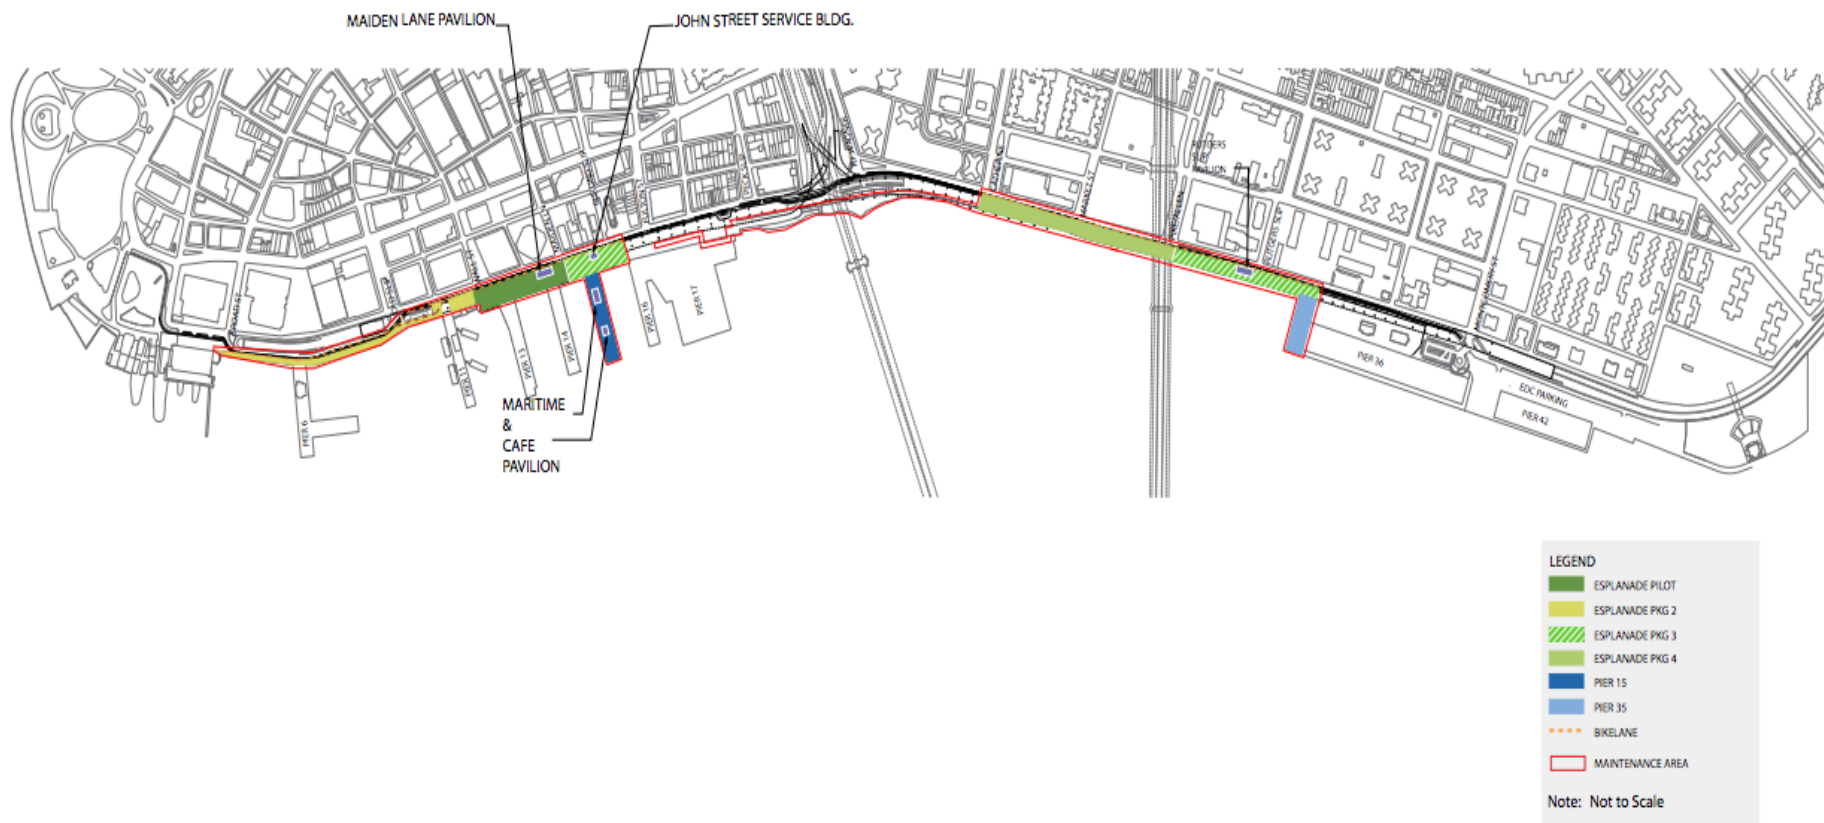

Recap from June Update

- Hunter Roberts procured as construction manager for Pier 35 and Package 4
- Package 4 in process of Waterfront Certification
- Brooklyn Bridge Esplanade in draft scope, plan to issue RFP for design



Work Update – Pier 35

- Currently in materials fabrication
 - Steel fabrication for structural support for screen wall began in August
- Mobilization for steel erector scheduled to begin in December
 - Currently executing subcontracts
- Targeted completion: Fall 2017



Work Update – Package 4

- **Catherine Street to Pike Slip**
 - DEP budgetary restrictions have prevented building on and within 30 feet of the water main
 - Procurement for elements outside of the water main will begin late this Fall
 - Includes seating, planting, surfacing, railing
 - DCP Waterfront certification expected in November
 - Expected completion end of 2017



Update – Brooklyn Bridge Esplanade

- **Peck Slip to Catherine Slip**
 - Currently working on a draft RFP and CP for design
 - Scope will take into account safety and permitting feasibility concerns in the Brooklyn Bridge Beach Feasibility Study
 - New project will incorporate design elements that bring the public closer to the water
 - Will schedule community visioning sessions to gather input



Timeline

Next Steps

- Construction of remaining elements
 - Pier 35: work to begin in December; expected completion Fall 2017
 - Package 4: Waterfront Certification in review by DCP, expected completion by end of 2017
- Brooklyn Bridge Esplanade Scope and RFP
 - Community visioning sessions to start next spring



Questions?

