

WEEKLY CONSTRUCTION BULLETIN

(5/12/25 – 5/18/25)

Brooklyn Facility Project PROJECT#: BBJ-KFAC BOROUGH: BROOKLYN DATE ISSUED: (5/9/25)

The following is an anticipated work schedule for the upcoming week. However, due to unforeseen field and weather conditions, it may become necessary to change some scheduled work locations, operations, and dates.


DATE(S)	WORK HOURS	LOCATION	OPERATION
5/12/25 – 5/17/25	M – F / 7:00 am – 12:00 am Sat / 9:00 am – 5:00 pm	(275 Atlantic Avenue)	Foundation construction (Noise / Vibrations / Excavating soil and installation of structural, electrical, and mechanical components for the crane and pouring concrete for building foundations / Backfill site floor in prep for slab-on-grade concrete pour / Work will take place inside the perimeter fencing)
5/16/25 – 5/18/25	Fri - Sun / 9:00 pm (Friday) – 11:59 pm (Sunday)	(275 Atlantic Avenue)	Tower crane #1 delivery and installation (Noise / Vibrations / Delivery of tower crane and installation on State St. by use of a Mobile Hydraulic crane. / State St. will be closed to vehicular traffic / Pedestrian access to State St. will remain. Flaggers will direct truck and crane operations and pedestrians / Work will be conducted throughout the weekend.)
5/12/25 – 5/17/25	M – F / 7:00 am – 12:00 am Sat / 9:00 am – 5:00 pm	(275 Atlantic Avenue)	Sidewalk shed construction (Noise / Construction of a sidewalk shed on Atlantic Ave. from Smith St. To Boerum Pl. / Noise, consistent traffic, and vehicular and pedestrian access restrictions. / Pedestrian walkway will be open from 7 am - 10 am with flaggers directing pedestrians as necessary. From 10 am - 6 pm, pedestrians will be directed across the perimeter of the site on Atlantic Ave. to accommodate the TPC work zone for utility tie-in work.)
5/12/25 – 5/17/25	M – F / 10:00 am – 6:00 pm Sat / 9:00 am – 5:00 pm	(275 Atlantic Avenue)	Atlantic Ave. utility tie-ins (Noise / Vibrations / Saw-cutting the roadway and jackhammering to excavate road materials to expose existing utility connections and install new utility tie-ins / Flaggers will direct pedestrian traffic as necessary)
5/12/25 – 5/16/25	M – F / 7:00 am – 5:00 pm	(275 Atlantic Avenue)	Debris and waste trucking (Noise / Removal of soil from the excavated site / Flaggers will direct pedestrian traffic as necessary)

(NO PARKING SIGNS: WILL BE DISTRIBUTED/POSTED 72 HOURS PRIOR TO THE TEMPORARY ELIMINATION OF STREET PARKING. PLEASE OBSERVE POSTED PARKING REGULATIONS IN CONSTRUCTION AREAS.

For further information: Contact **Lucien Allen**, the **Community Construction Liaison** at (917) 270 - 2370 or BrooklynCCL@bbjnyc.com

Eric Adams,
Mayor

Thomas Foley, P.E.
Commissioner

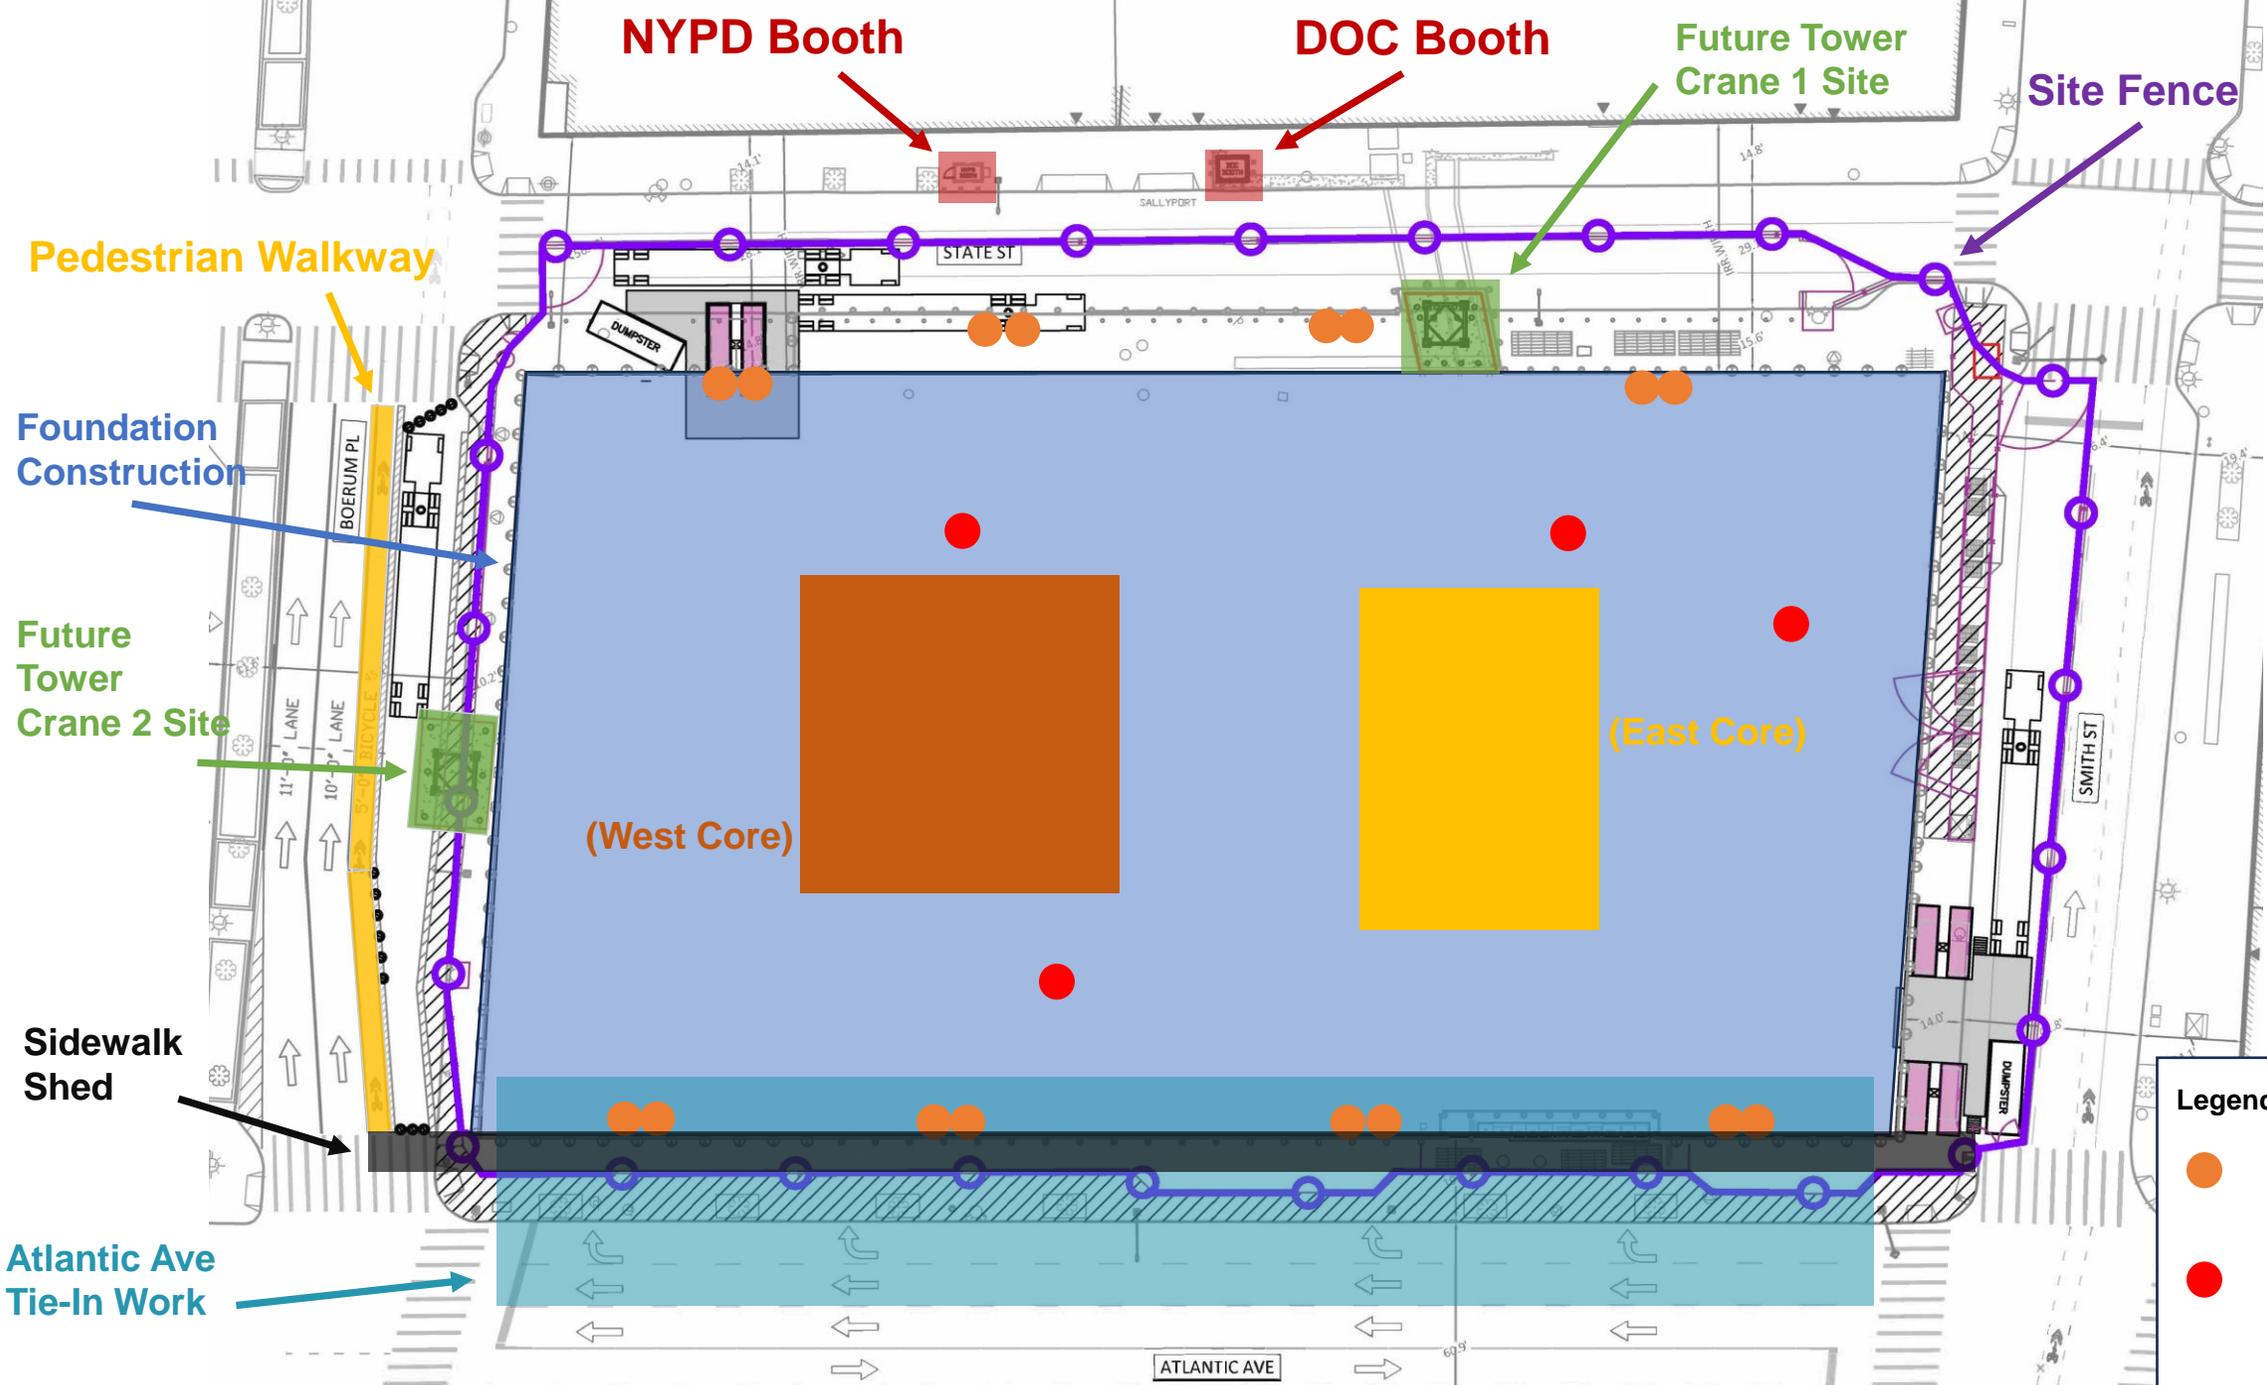

- Legend**
- Lighting fixtures in fixed position
 - Movable lighting fixtures (*position tentative as work progresses*)
