BMCR | Project Area and Flood Protection Design

Project Details Jacobs/GPI JV **Program Management Construction** Management (PMCM)


John P. Picone Inc.

Contractor - NTP issued October 2022

2023 through 2026 Timeline

\$349 Million


Budget

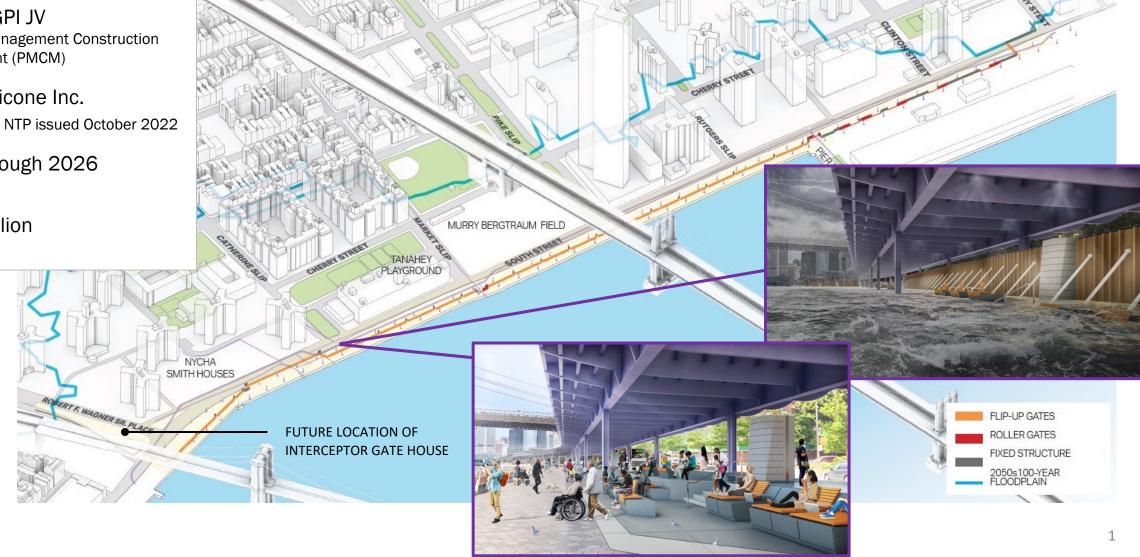



ESCR | Project Overview

FLOOD PROTECTION ALIGNMENT

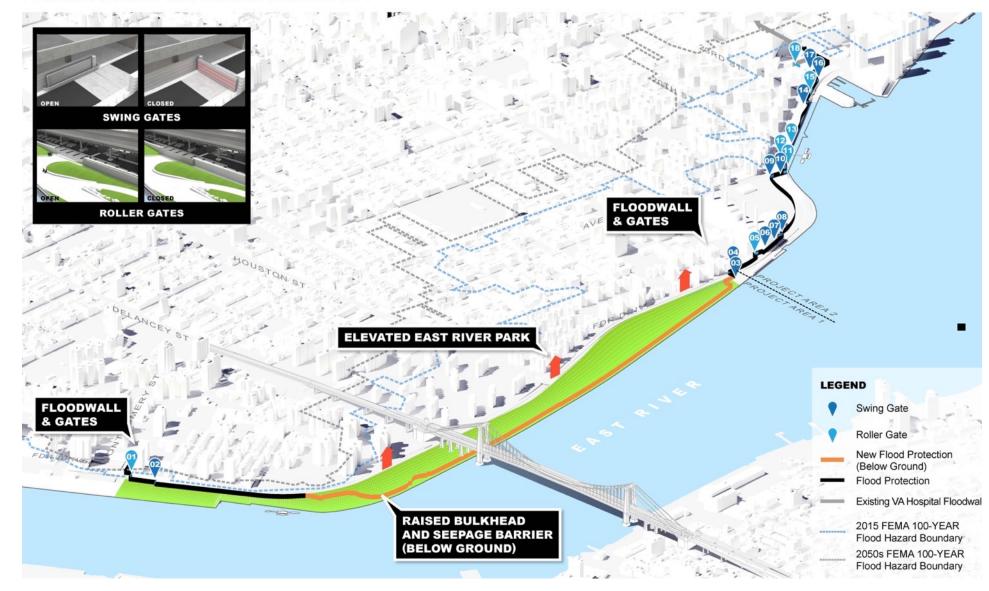





ESCR | Overview of Contracts

Project Area 1 (PA1)

Budget: \$1.27 Billion

Contractor: IPC Resiliency Partners

• *NTP:* issued August 16, 2021

On time for 2026 Completion

Project Area 2 (PA2)

• Budget: \$163 Million

 Contractor: Perfetto Contracting Co. Inc.

NTP: issued November 2020

• On time for 2025 Completion


Parallel Conveyance (PC)

• Budget: \$155 Million

Contractor: NYCC-JPL JV


• *NTP:* issued September 13, 2022

• On time for 2026 Completion

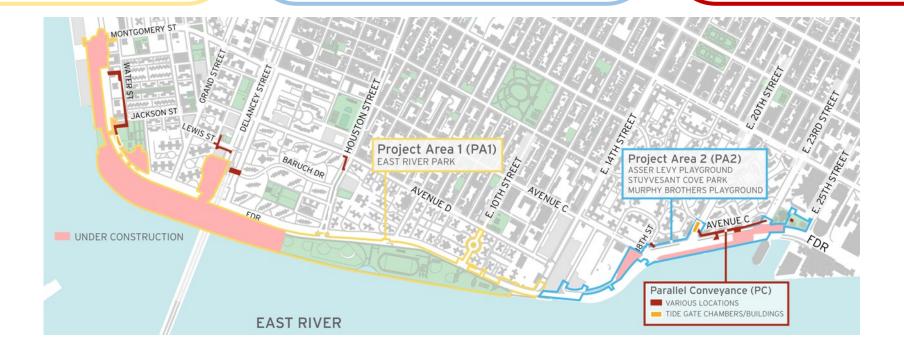




ESCR | PA1 & PA2 Construction Progress

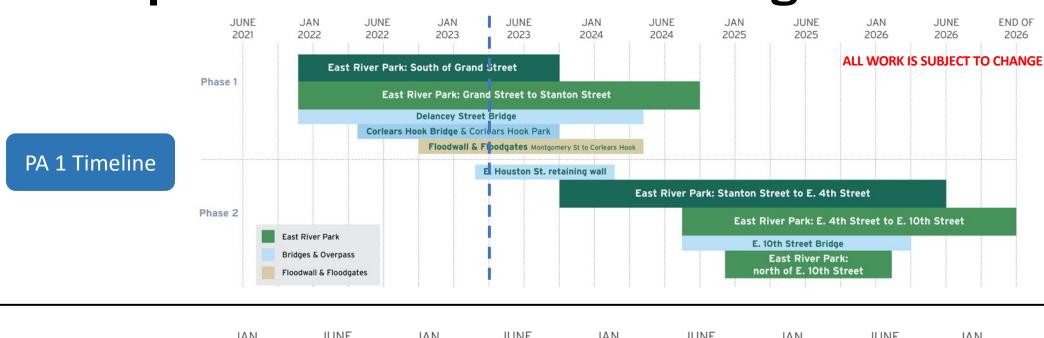

PA 2 Timeline






Completion of Flood Walls and Gates in Project Area 2

ESCR | PA1 & PA2 Construction Progress





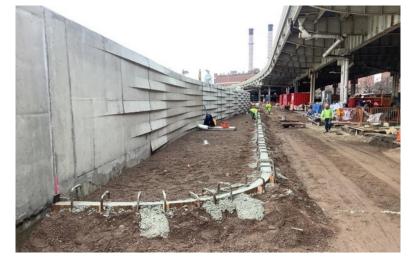

Floodgate, Asser Levy Playground, Flood wall









Sheet pile, Combi Wall, Sewer expansions

5

ESCR | Community Engagement





ESCR Community Call for Art Program – May 2022











ESCR flyers, Community Tabling - September 2022, Work With Us Event - October 2022

