


COMMUNITY ADVISORY GROUP (CAG)

Meeting #25

**East Side Coastal
Resiliency (ESCR)
Project**

Zoom Conference Call
Thursday September 29, 2022 | 4:00 pm

Project Area Overview

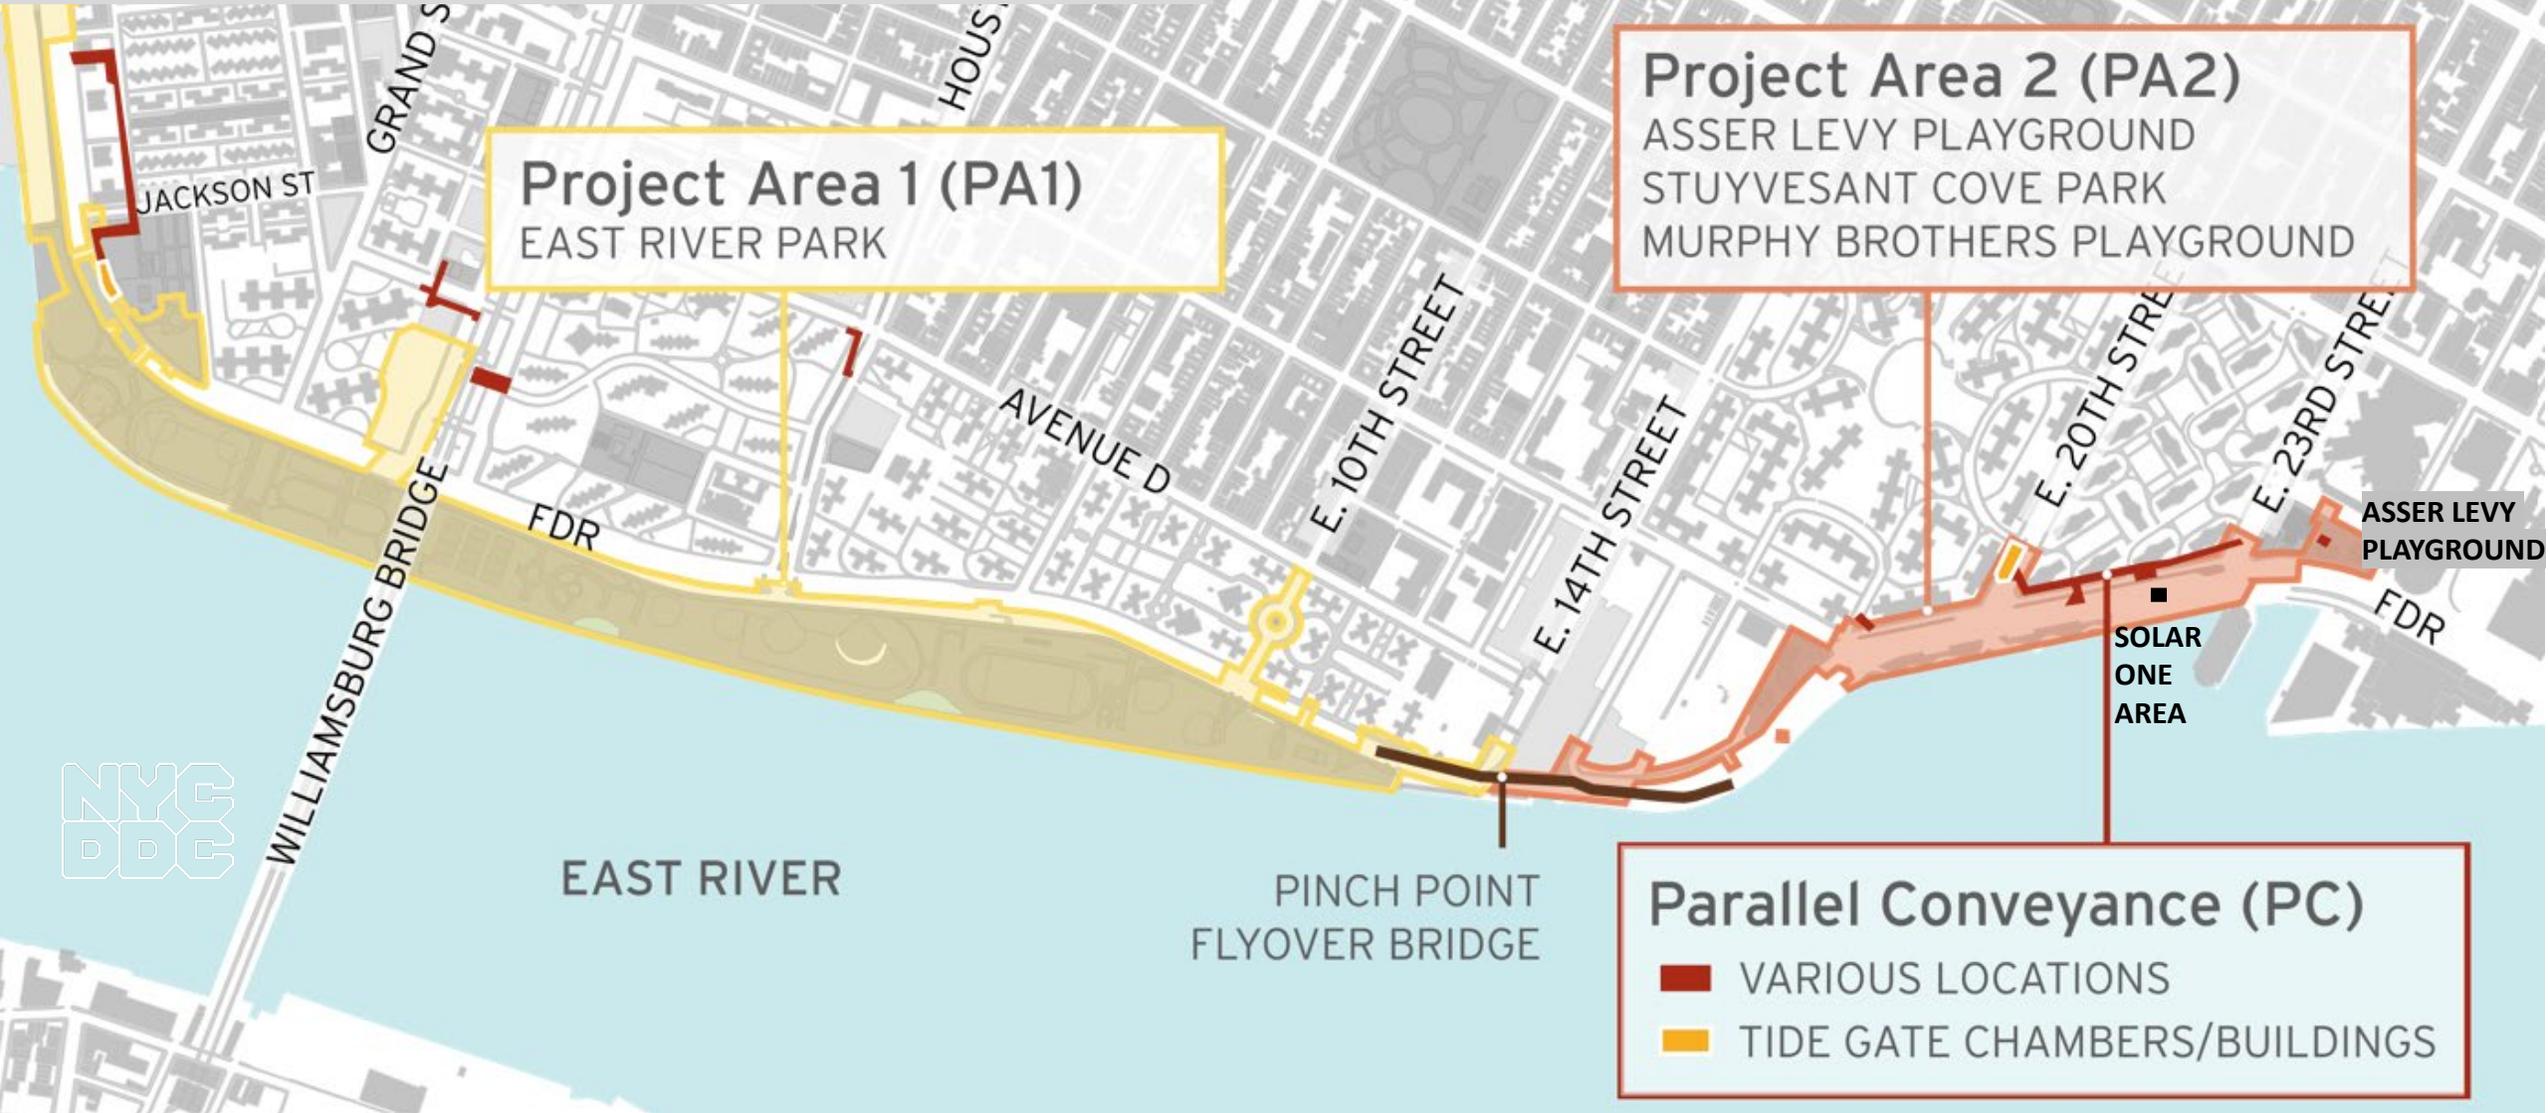

ESCR FOCUS AREA TOPICS

**CONSTRUCTION
PROGRESS/
APPROACH**

ENVIRONMENT

**ACCESS/
SIGNAGE/
SAFETY**

**PARK
AMENITIES**

**HIRING
COMPLIANCE**

**PROJECT
INFORMATION
DELIVERY**

**COMMUNITY
PROGRAMMING &
COORDINATION**

QUESTIONS?



ESCR Work With Us Events



[Henry Street Settlement's Jobs Plus In-Person Job Fair](#)

October 4, 2022, 2pm – 5pm

Henry Street Settlement's Jobs Plus Program will be hosting an indoor Job Fair and would like to invite employers to meet member candidates for available positions at your companies.

Please note all office spaces and restrooms have PPE (i.e. hand sanitizer, masks), Covid screener and social distancing guidelines are strictly enforced.

**EAST SIDE
COASTAL
RESILIENCY**

[ESCR Quarterly Information Session: In-Person Career Pathways Event](#)

October 19, 2022, 4:30pm – 7:30pm

Work with us in-person, Quarterly Information Event on Career Pathways Exploration within the ESCR Project. Design, administration and construction careers will be featured.



[The 28th Annual 2022 Competitive Edge Conference](#)

October 31, 2022, 9am – 3pm

The must-attend event for MWLBE | DBE | SDVOB | Prime Contractors

Since 1993, the Competitive Edge Conference has linked the region's small businesses, including MWLBES and Locally Based Enterprises, with leading decision-makers across industries.

Pier 60 Chelsea Piers, NY



**HIRING
COMPLIANCE**

ESCR Work With Us

Careers & Procurement

The ESCR project team is committed to working with M/WBE and Section 3 firms. As we onboard our contractors, we continue to assess workforce needs.

Current Job and Contracting Opportunities

- 001 - Printing Shop/Print Services (HNTB-LiRo)
- 003 - Senior Inspector (HNTB-LiRo)
- 004 - Inspector II (HNTB-LiRo)
- 005 - Office Engineer (HNTB-LiRo)
- 006 - Assistant Office Engineer (HNTB-LiRo)
- 009 - Administrative Assistant (IPC)
- 010 - Payroll Specialist (IPC)

View [job descriptions](#) and apply through our [online portal](#).

Visit the New York City Department of Design and Construction's (NYCDDC's) procurement site for other opportunities related to the ESCR project as they are made available.

- [Find careers with NYCDDC](#)
- [Work with DDC](#)

<https://www1.nyc.gov/site/escr/contact/work-with-us.page>

Have a Question on Hiring?

https://pima.ddccr.com/public/comment/project-comment-dynamic?project_id=14047&pe_id=2565

****Next hiring update will be provided in October**



Project Area Overview

Project Area 2 & Project Area 1 Construction Updates

Air Quality Monitoring Update

Project Area Overview

Project Area 1 (PA1)

- NTP issued August 16, 2021
- Partial Closures:
 - East River Park south of Stanton St.
 - Greenway closure to E. 10th St.
 - Corlears Hook Park & passive lawn
- Delancey St. & Corlears Hook pedestrian bridges removed. Corlears Hook temp ped Bridge installed.
- ongoing ConEd Work
- esplanade removal, soil stabilization and deep sewer work in progress
- floodwall construction activities begin around Montgomery Street

Project Area 2 (PA2)


- NTP issued November 2020
- Asser Levy Playground Open
 - Gate 18 installed
- Stuyvesant Cove Park including Solar One Area under construction
 - over 1,000 ft of floodwall installed
 - Gate 14 installed
 - site restoration north of E 20th St. underway
 - floodwall construction in progress north of E 20th St. underway
- **Murphy Brothers work started September 26, 2022**

Parallel Conveyance (PC)

- contract awarded in May to NYCC JPL JV
- NTP issued September 13, 2022
- construction start anticipated in winter 2022
- contract duration is approximately 4 years

**CONSTRUCTION
PROGRESS/
APPROACH**

PA2 | Construction Progress

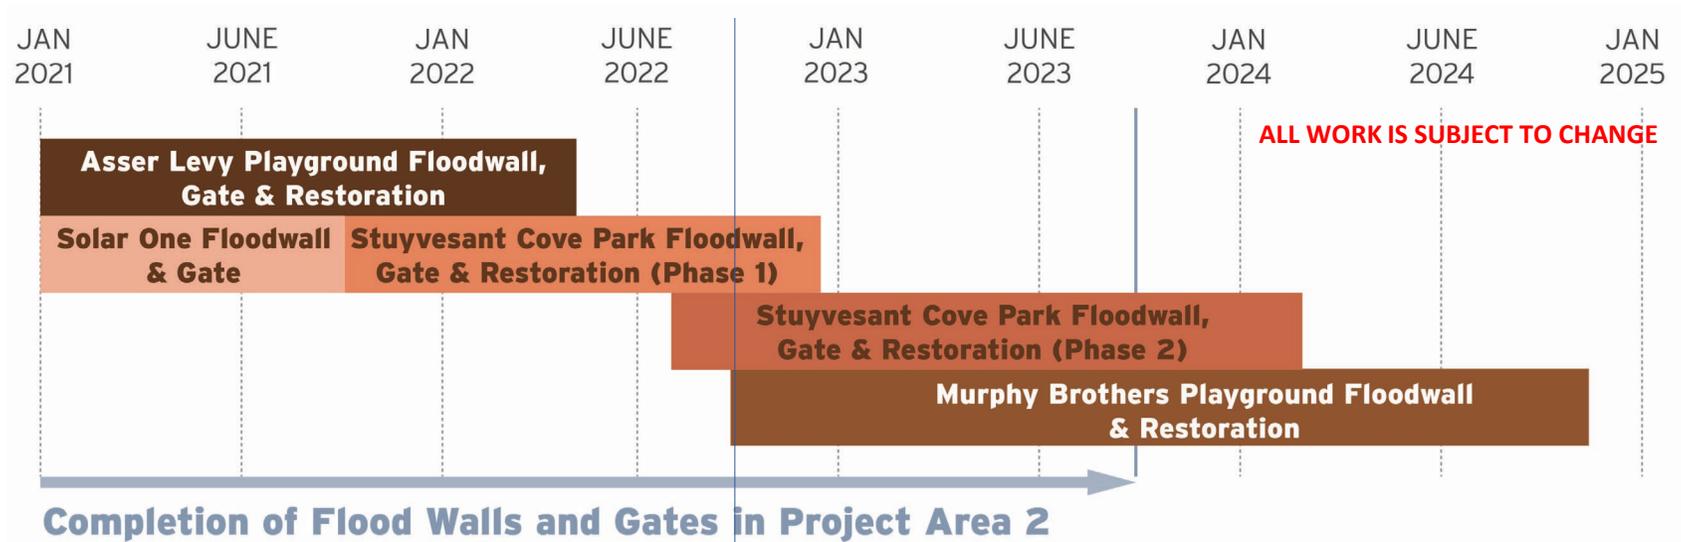

**ACCESS/
SIGNAGE/
SAFETY**

PA2 | Current Greenway Access





PA2 | Greenway Access Look-ahead

Mid-Late October 2022

- in coordination with DOT
- Greenway from E 20th St heading north will reopen
- Greenway from E20th St south will close for Stuy Cove Park Ph. 2 (advisory will be issued)
- Ferry access will remain open
- More details and dates to follow



**CONSTRUCTION
PROGRESS/
APPROACH**

PA1 | Construction Progress



PA1 | October 2022 Construction Activities

ALL WORK IS SUBJECT TO CHANGE

1. Soil stabilization activities and esplanade dismantling along the waterfront.
Deep sewer activities and pile install.
Delancey Street utility, pile and abutment work (park side).
2. Corlears Hook Park pile installation for new bridge.
3. Passive lawn partial closure for utility work.
4. ConEd utility work near Montgomery Street & South Street.
5. **Montgomery St. – Cherry St. Greenway floodwall activities.**
6. **Amphitheater asbestos abatement ongoing**
7. ConEd work in Shared Use Path E. Houston Street to E. 10th Street will continue through Q2 2023.
Slip Ramps in use.
8. Ongoing partial FDR lane closures continue at various locations.

Weekly Bulletins & Advisories are issued with construction activities.
Saturday work is anticipated for some work operations as indicated.



PA1 AQM | August 2022 Update

Work activities at East River Park focused on soil stabilization, deep sewer excavation and esplanade removal along the waterfront. Corlears Hook bridge removal activities and start of pile work. Delancey Street Bridge start of pile work on park side. ConEd utility work along Greenway, at E 10th Street and Avenue D and at Montgomery Street. Nightwork site prep operations around Montgomery Street for the start of floodwall construction operations started. Start of Amphitheater asbestos abatement towards end of the month.

The PM daily value (24-hour TWA) did not surpass the PEL for the month of August.

Levels of Particulate Matter surpassed the PEL for 15-min TWA on 16 occasions:

- PM 10 levels surpassed the PEL on 8/13, 8/16, 8/17, and 8/25, all for 20 minutes or less, and on 8/26 for 40 minutes.
- PM 2.5 levels surpassed the PEL on 8/5, 8/10, 8/12, 8/13, 8/17, 8/25, and 8/26, all for 18 minutes or less.
- Construction activity was closely monitored, and dust mitigation techniques were continuously implemented to contain airborne particles due to construction activities.

PA2 AQM | August 2022 Update

Work activities at E23rd Street focused on floodwall construction. At Stuyvesant Cove Park north, work focused on park reconstruction and at Stuyvesant Cove south, work focused on clearing and pile installation.

The PM daily value (24-hour TWA) did not surpass the PEL for the month of August.

Levels of Particulate Matter surpassed the PEL for 15-min TWA on 2 occasions:

- ALP-S1 and S2 - PM2.5 and PM10 levels surpassed the PEL on 8/12 for 58 minutes due to staged trucks for asphalt paving operations. Flaggers directed the public away from the trucks.
- ALP-S2 - PM2.5 and PM10 levels surpassed the PEL on 8/18 into 8/19 after hours when there was no construction activity.
- Construction activity was closely monitored, and dust mitigation techniques were continuously implemented to contain airborne particles due to construction activities.

ACCESS/
SIGNAGE/
SAFETY

What We've Heard

- **Lighting:** PA1 around track




6th St south of Track



near Track south gate



near Track north gate

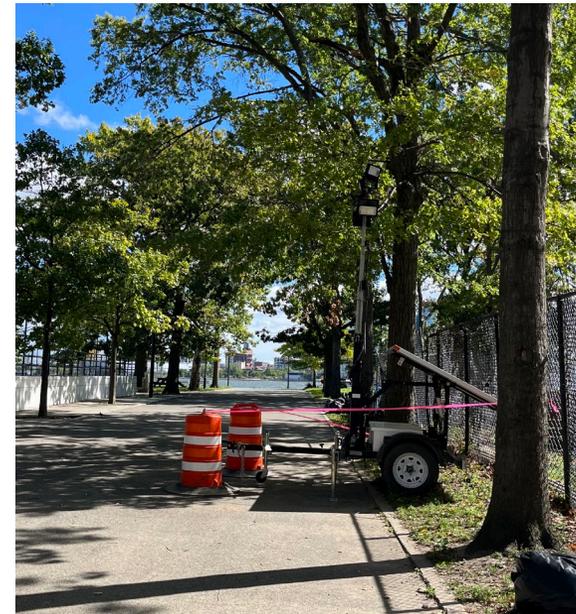

8th St north of Track

