

East Side Coastal Resiliency Construction Update

CB3 Parks Committee Meeting
BRC Senior Services Center
30 Delancey Street
June 11, 2026



Highlights

- Employment Resources
- Overview of Contracts
- Construction Updates
 - PA1 Construction Activities
 - PA1 Outreach
 - Call for Art
 - What We've Heard
 - PC Construction Activities



ESCR Tabling & Community Events
Reach out to project CCLs to schedule!

[ESCR to YOUR School](https://nyc.gov/escr)

Employment Resources

Quarterly ESCR Employment Resource Fair on
Thursday, June 4, 2026

- 85 attendees (of 224 registrants)
- 11 organizations represented, including NYCHA REES, Workforce1, Henry Street Settlement, Jobs Plus, New York State (NYS) Department of Civil Service, NYS Department of Labor, and IPC Resiliency Partners
- Planned in collaboration with Catholic Charities, and hosted at St. Mary's Church on Grand St.

**Thank you to all our attendees
and partners!**




*ESCR construction updates and program information provided at
Employment Resource Fair, June 2026*



Quarterly Employment Resource Fair, June 2026

Overview of Contracts & Construction Updates

Project Area Overview

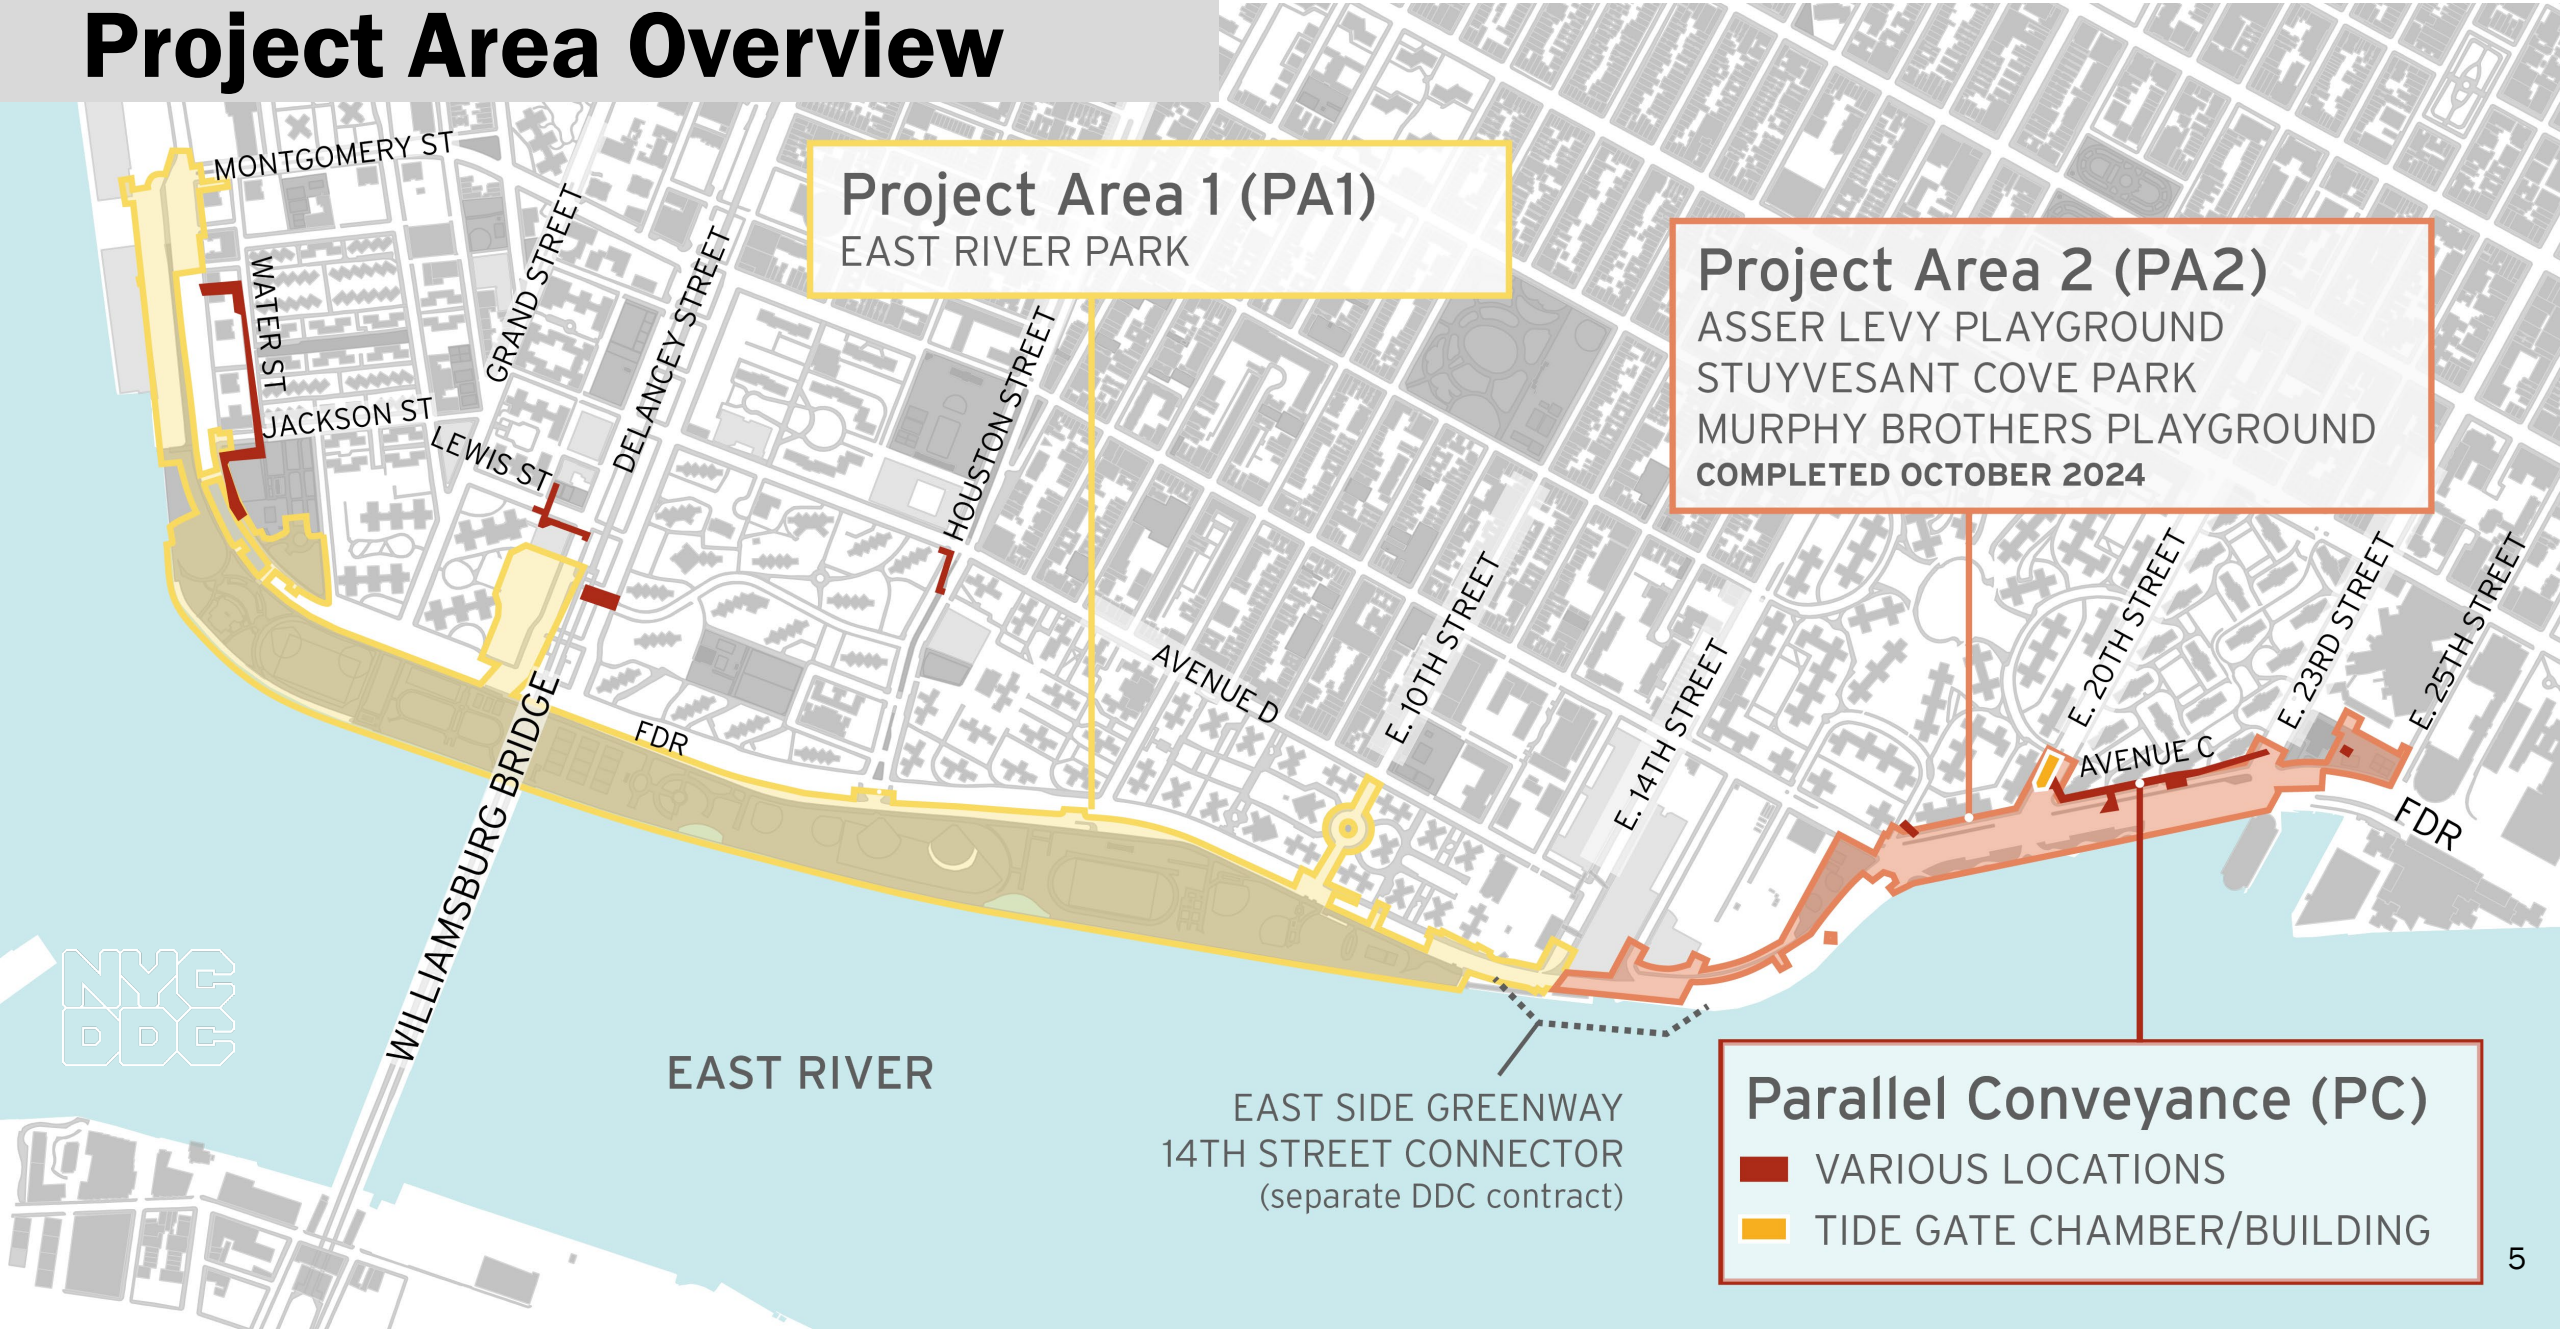

Snapshot of Contracts

Project Area 1 (PA1)

NTP issued August 2021

- **Open Areas:**
 - East River Park Amphitheater
 - Ballfields 1 & 2
 - Basketball Courts
 - Nature Exploration and Water Play
 - Picnic and BBQ
 - 12 Tennis Courts
 - Adjacent esplanade areas
- **Closed Areas:**
 - East River Park north of Tennis Courts
- **Park Access:**
 - Delancey St. bridge: **Open**
 - Corlears Hook bridge: **Open**
 - Pier 42 connection: **Open**
 - Houston St. entry, E. 6th Street bridge, E. 10th Street bridge: **Closed**

Parallel Conveyance (PC)

NTP issued September 2022

- **Corlears Hook Park area**
 - Water Street
 - Jackson Street
 - South Street
 - Corlears Hook Park
- **Williamsburg Bridge area**
 - Broome Street
 - Lewis Street
 - Delancey Street South
 - Delancey Street North
 - Baruch Drive
- **E. Houston and Columbia Streets**
- **E. 18th St. and Avenue C**
- **E. 20th St. and Avenue C**

Project Area 2 (PA2)

NTP issued November 2020, substantial completion 2024

- **Asser Levy Playground:** **Open**
- **Stuyvesant Cove Park:** **Open**
 - E. 23rd Street entrance: **Open**
- **Murphy Brothers:** **Open**
- All 3,129 ft of floodwall installed
- All Gates 7-18 installed

VISIT PA1 GALLERY:

<https://www.nyc.gov/site/escr/project-updates/pa1-gallery.page>

VISIT PA2 GALLERY:

<https://www.nyc.gov/site/escr/project-updates/pa2-gallery.page>


VISIT PC GALLERY:

<https://www.nyc.gov/site/escr/project-updates/pc-gallery.page>

PA1 | Construction Activities

ALL WORK IS SUBJECT TO CHANGE

1. Floodwall and floodgate operations.
2. Construction of Parks maintenance & tennis buildings.
Utility work.
3. Esplanade reconstruction, E. Houston Street retaining wall activities.
Clean fill installation.
4. Deep sewer work, floodwall construction, and excavation.
5. Utility work.
Mobilization of equipment for E. 10th Street bridge.
Preparation for E. 13th Street floodwall construction.
6. Phase 1 amenities **OPEN**.
Delancey Street & Corlears Hook bridge work.
7. Ongoing partial FDR lane closures continue at various locations for bridge work and utility installations.

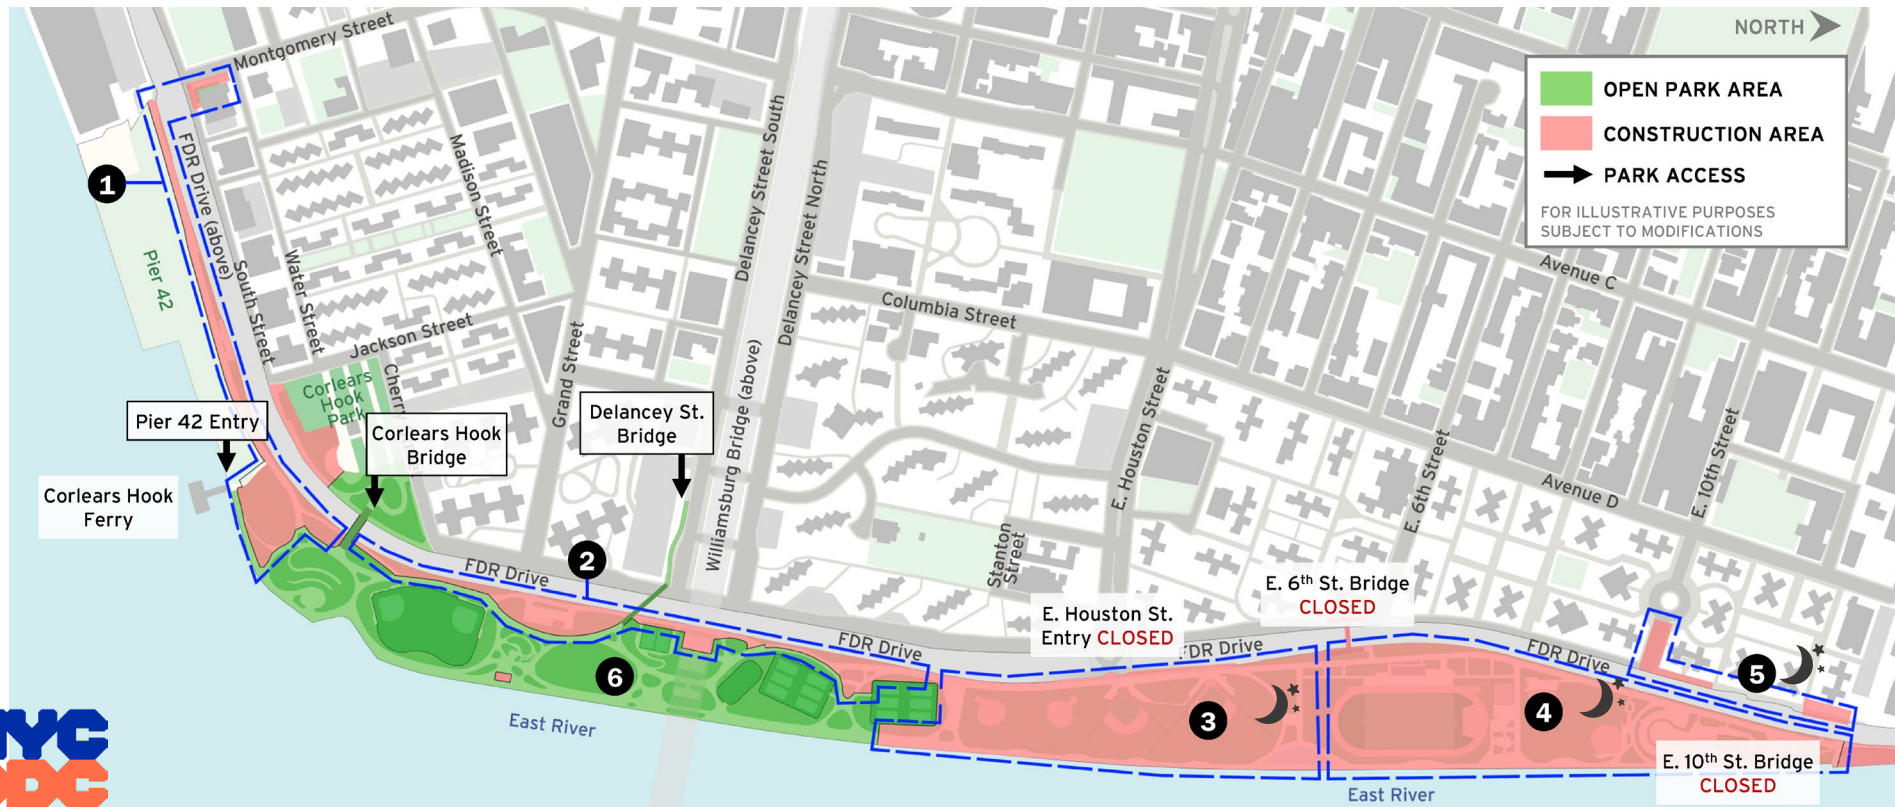

★ INDICATES NIGHT WORK SHIFTS

Weekly Bulletins & Advisories are issued with construction activities.

Saturday work is anticipated for some work operations as indicated.

PA1 | E. 10th St. Bridge Construction

ALL WORK IS SUBJECT TO CHANGE



PA1 | E. 10th St. Bridge Construction


ALL WORK IS SUBJECT TO CHANGE



PA1 | E. 10th St. Bridge Construction

ALL WORK IS SUBJECT TO CHANGE


- Construction phasing (approx. 12-14 months total):
 1. Work and staging area mobilization
ONGOING for 1-2 weeks
 2. Installation of ramp and abutment piles
Anticipated to begin in late-June / early-July,
ongoing for 2-3 months
 - Piles will be pre-drilled and vibrated to an extent to reduce impact on residents, though this will still be a noisy and disruptive daytime operation
 3. Assembly of bridge on E. 10th Street (2 months)
 4. Bridge placement (1 night)
 5. Construction of ramps (6-7 months)

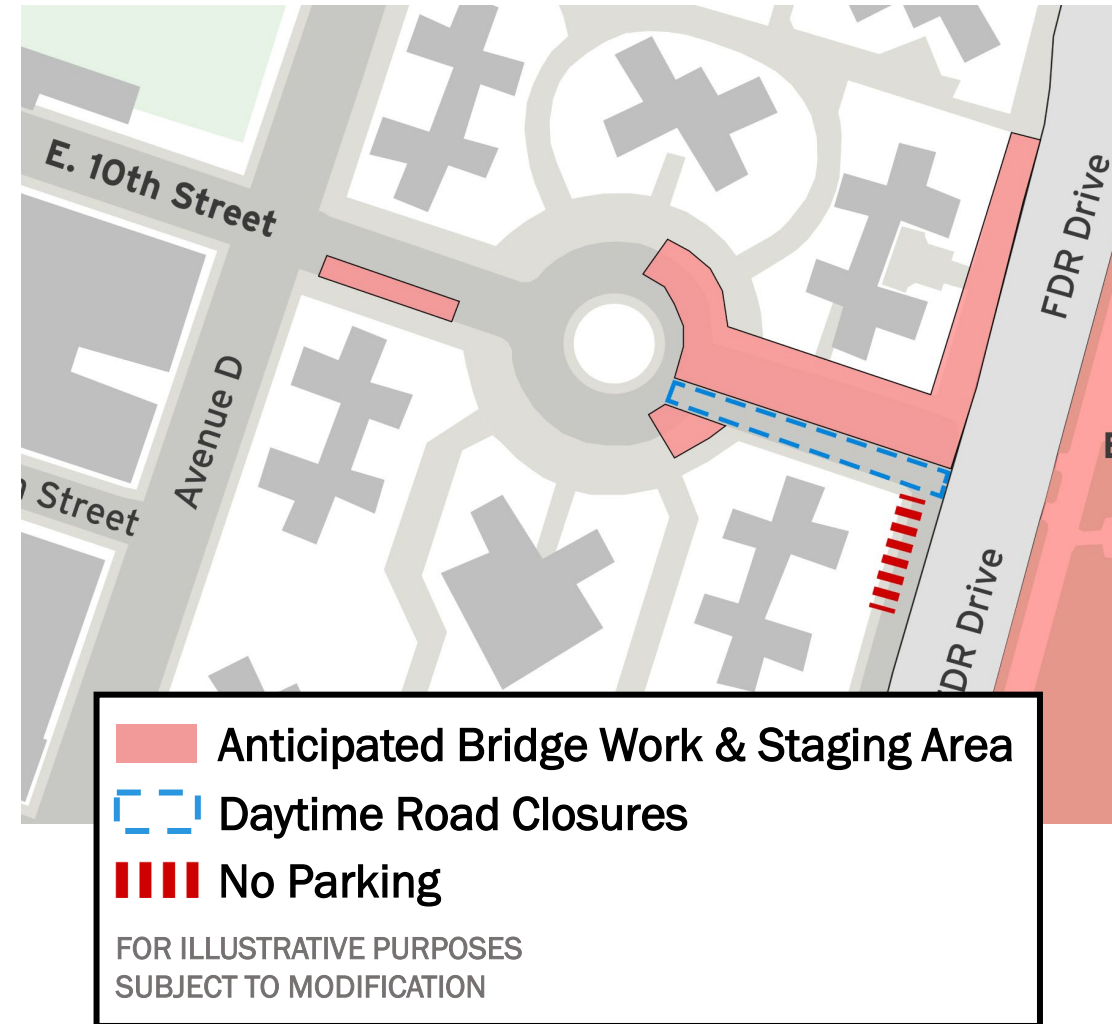

PA1 | E. 10th St. Bridge Construction

ALL WORK IS SUBJECT TO CHANGE

- Building access will be maintained at all times
- Access to FDR Drive Service Road will be limited during the day to ensure safety of public and workers during certain operations
- Parking at E. 10th Street and FDR Drive Service Road will be limited to ensure safe passage of emergency vehicles

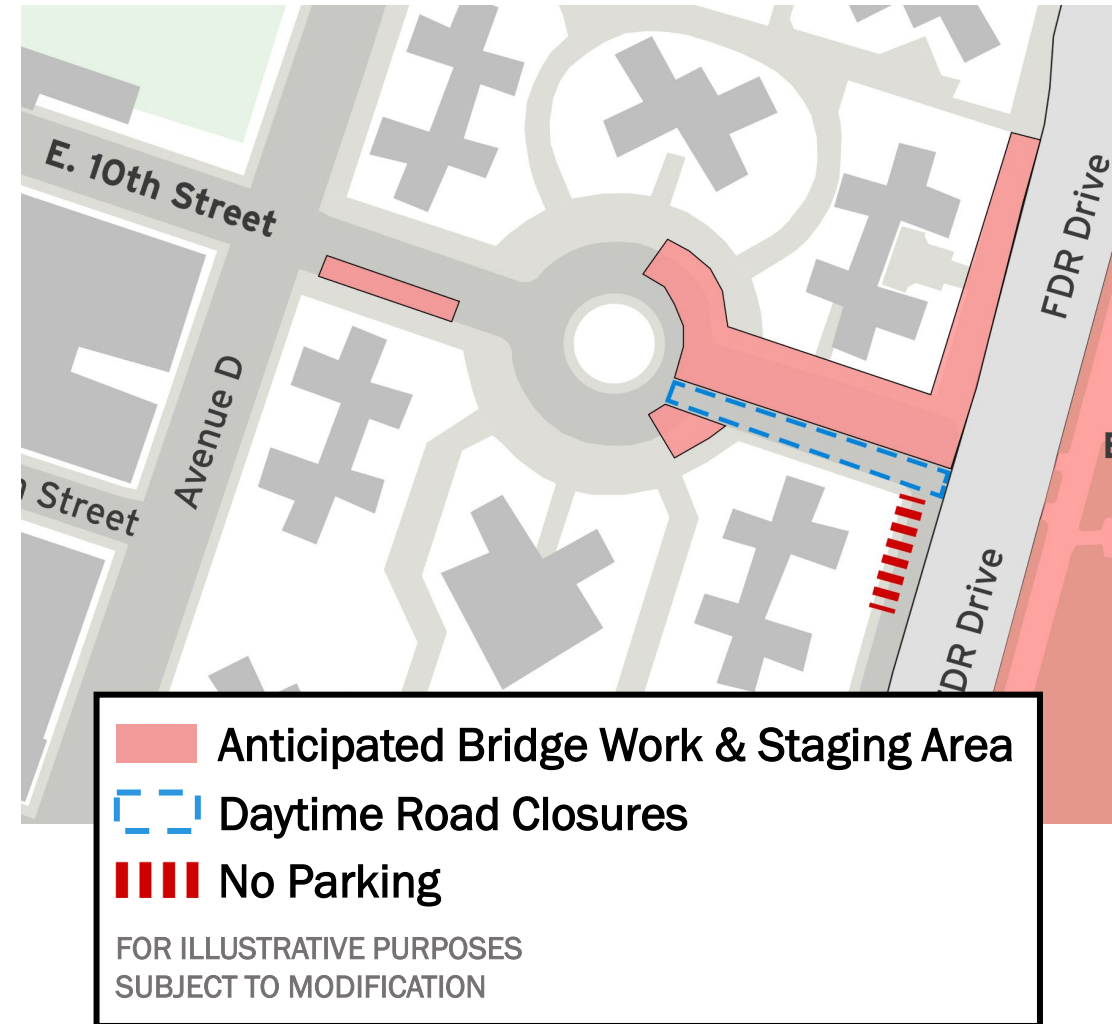

PA1 | E. 13th St. Flood Protection Construction


ALL WORK IS SUBJECT TO CHANGE



PA1 | E. 13th St. Flood Protection Construction

ALL WORK IS SUBJECT TO CHANGE


- Water main work anticipated to begin late-June
 - Water main work will require a brief water shutdown, with water restored at the end of the day
 - CCLs will provide 72-hour notice before shutdown in English, Spanish, and Chinese

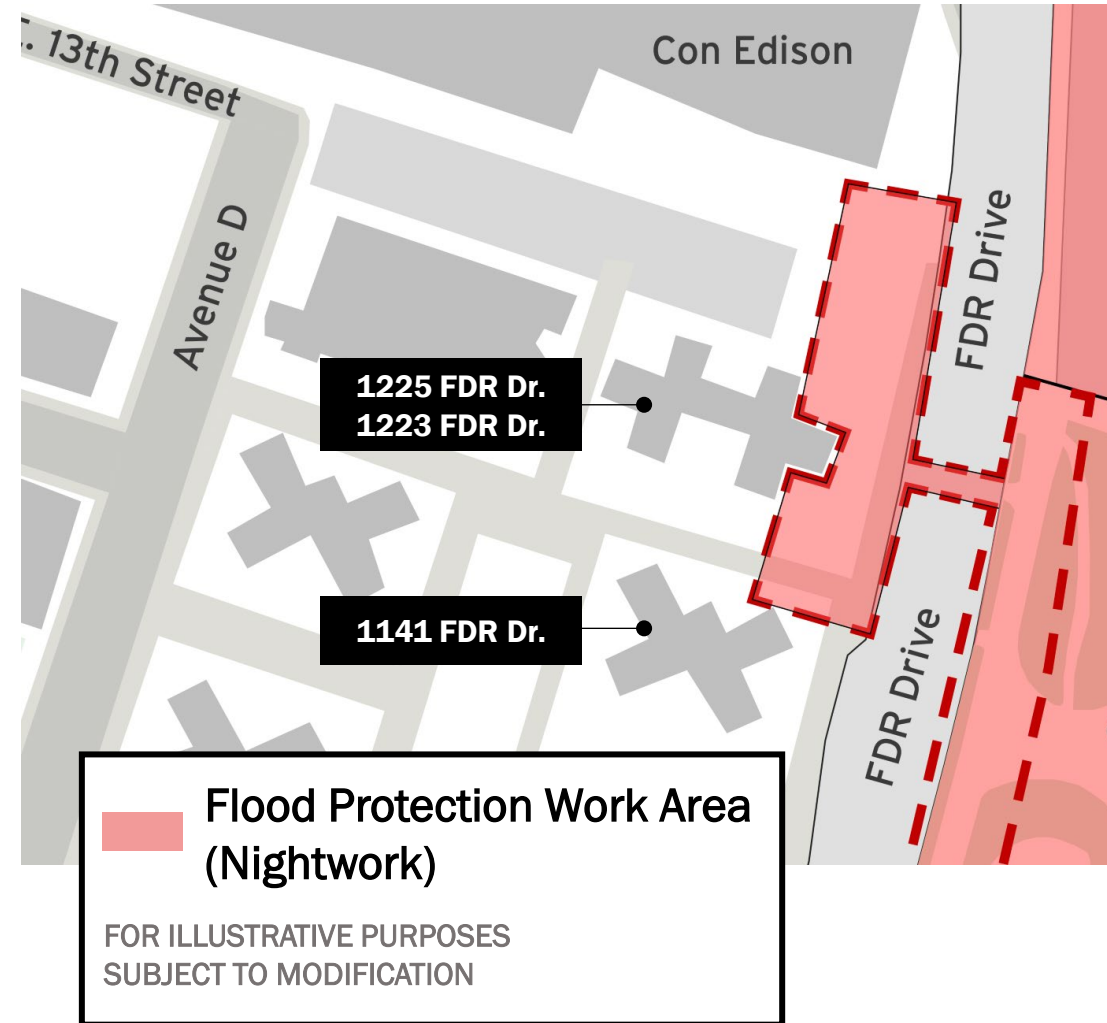

PA1 | E. 13th St. Flood Protection Construction

ALL WORK IS SUBJECT TO CHANGE

- Underground floodwall infrastructure will be **drilled** into the ground east of FDR (in East River Park) & west of FDR (near Riis)
- Underground infrastructure for floodgates crossing the FDR Drive will be **driven**, which is a noisy and disruptive operation
 - Noise monitors in place and additional mitigation opportunities being explored
 - Anticipated to take approximately two months
- Unfortunately, this work is required by DOT to be performed at night (roughly 10pm to 6am)
- Anticipated to begin late-June / early-July
- When dates are confirmed, we will provide as much advance notice as possible via formal advisories and at nyc.gov/escr/nightwork

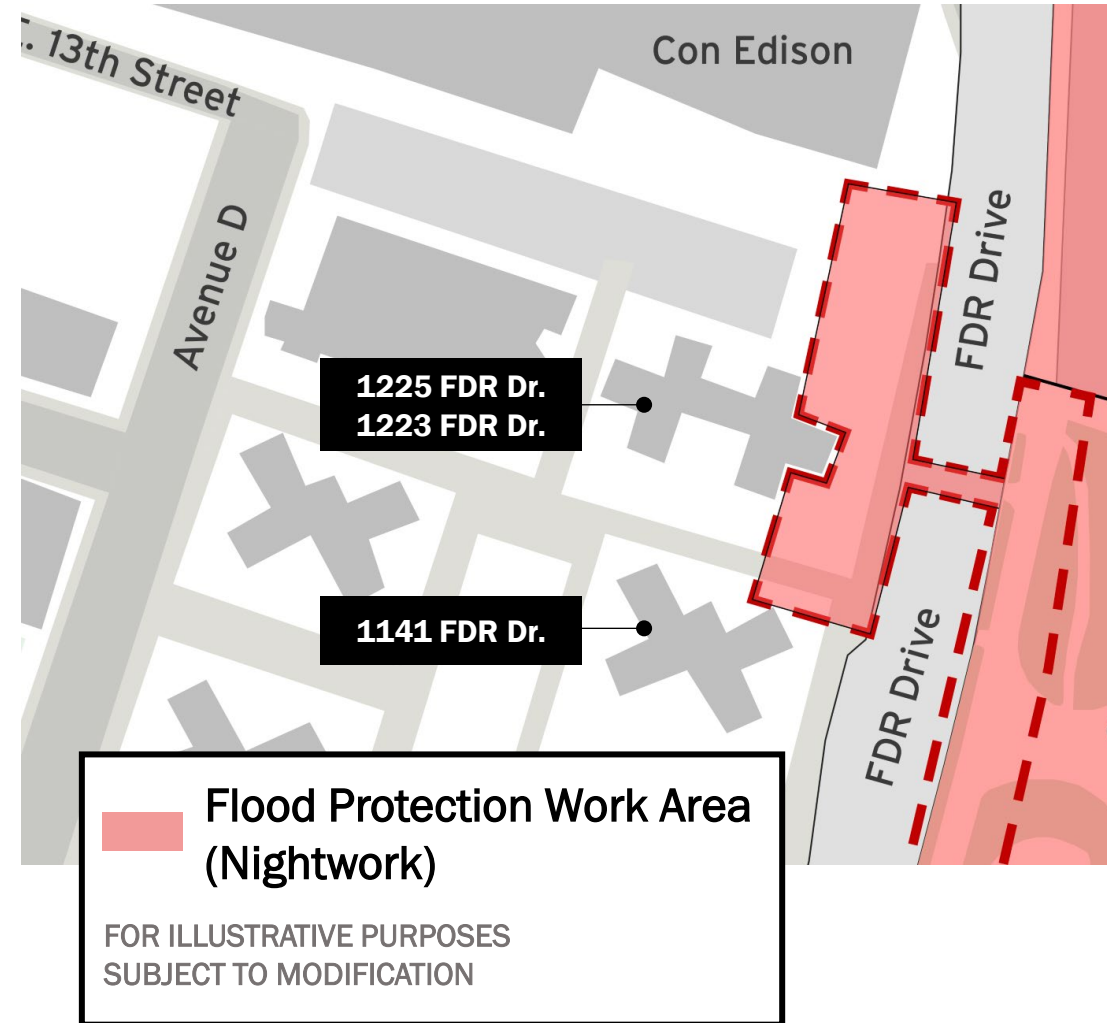

PA1 | What We've Heard

ALL WORK IS SUBJECT TO CHANGE

Nightwork

- DOT OCMC's nightwork policy: "due to high traffic volume in both direction of the FDR, lane closures will only be permitted in the overnight hours. This applies to everyone including our in-house crews except for an emergency that jeopardize the safety of the travelling public."

PA1 | Targeted Outreach for Upcoming Work

- Engagement team attending all Riis TA meetings
- Will schedule virtual meeting(s) as schedule is finalized
- Updates related to nightwork to be provided dedicated web page: nyc.gov/escr/nightwork.
- Ongoing coordination with NYCHA re: email blasts to residents.
- We appreciate any support community leaders and elected officials are able to provide in communicating project updates to residents



Riis TA Meeting, June 2026

PA1 | Targeted Outreach for Upcoming Work

April:


- 4/14/26 – Riis Tenant Association Meeting
- 4/15/26 – CCL Flyering at Riis Pantry
- 4/23/26 – Community Advisory Group Presentation / Meeting
- 4/29/26 – CCL Flyering at Riis Pantry

May:

- 5/4/26 – CCL Flyering at Riis
- 5/5/26 – Riis Construction Updates Presentation (Virtual)
- 5/6/26 – CCL Flyering at NYCHA Riis
- 5/7/26 – Riis Construction Updates Presentation (Virtual)
- 5/12/26 – Riis Tenant Association Meeting
- 5/13/26 – CCL Flyering at Riis Pantry
- 5/19/26 – PSA4 Construction Updates Presentation
- 5/20/26 – Tabling at Jobs Plus Community Resource Fair
- 5/28/26 – Community Advisory Group Presentation / Meeting

June:

- 6/9/26 – Riis Tenant Association Meeting
- 6/10/26 – CCL Flyering at Riis Pantry



Virtual meetings recorded and posted online, May 2026



Riis Housing Pantry, May 2026

PA1 | Call for Art 2026



Call for Art panels displayed at E. Houston Street, 2024

PA1 | Call for Art 2026


- Invitation for community members to submit visual artwork to be printed on construction fencing, with an emphasis towards residents of NYCHA Riis.
- Themes:
 - What stories, cultures, and identities make NYC's waterfront unique?
 - What does climate resiliency mean to you?
- Email ESCRCL1@ddccr.com to make digital submission or arrange a pick-up; or submit at a drop-off location
- Flyers available in English, Spanish, and Chinese
- Deadline for submissions: October 16, 2026



Call for Art website:
on.nyc.gov/4egUBPI



PA1 | Call for Art 2026

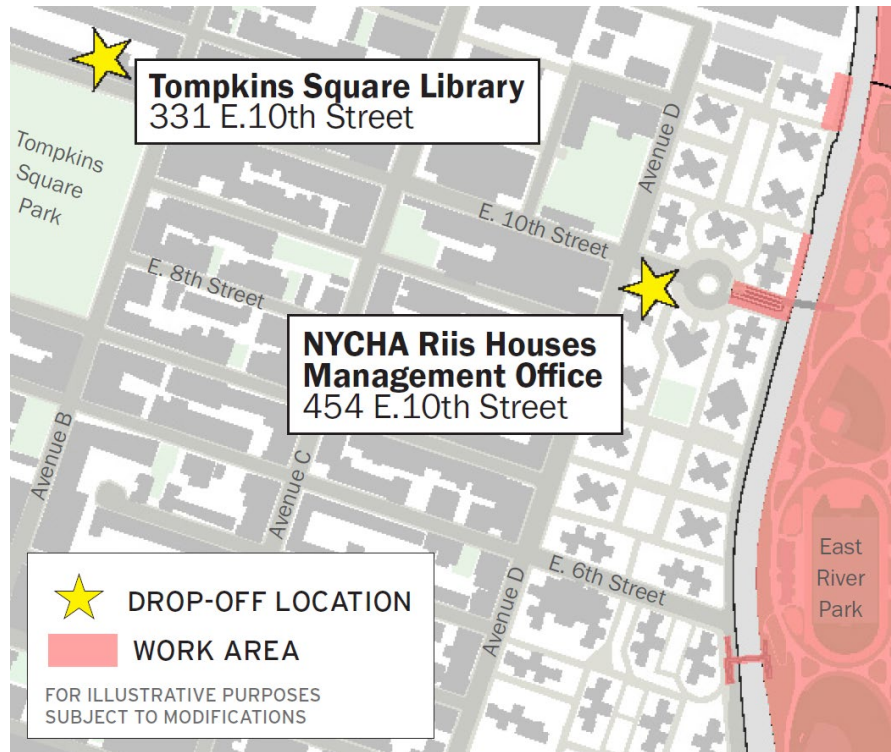

Call for Art website:
on.nyc.gov/4egUBPI



Riis Management
Office Drop Box



Tompkins Square
Library Drop Box

PA1 | Construction Photos



Eastern abutment for E. 10th Street bridge – June 2026



PA1 | Construction Photos



Waterproofing applied to tennis building – June 2026




Tennis building construction – June 2026

PA1 | Construction Photos



Installation of H-piles for sewer support near track area – June 2026

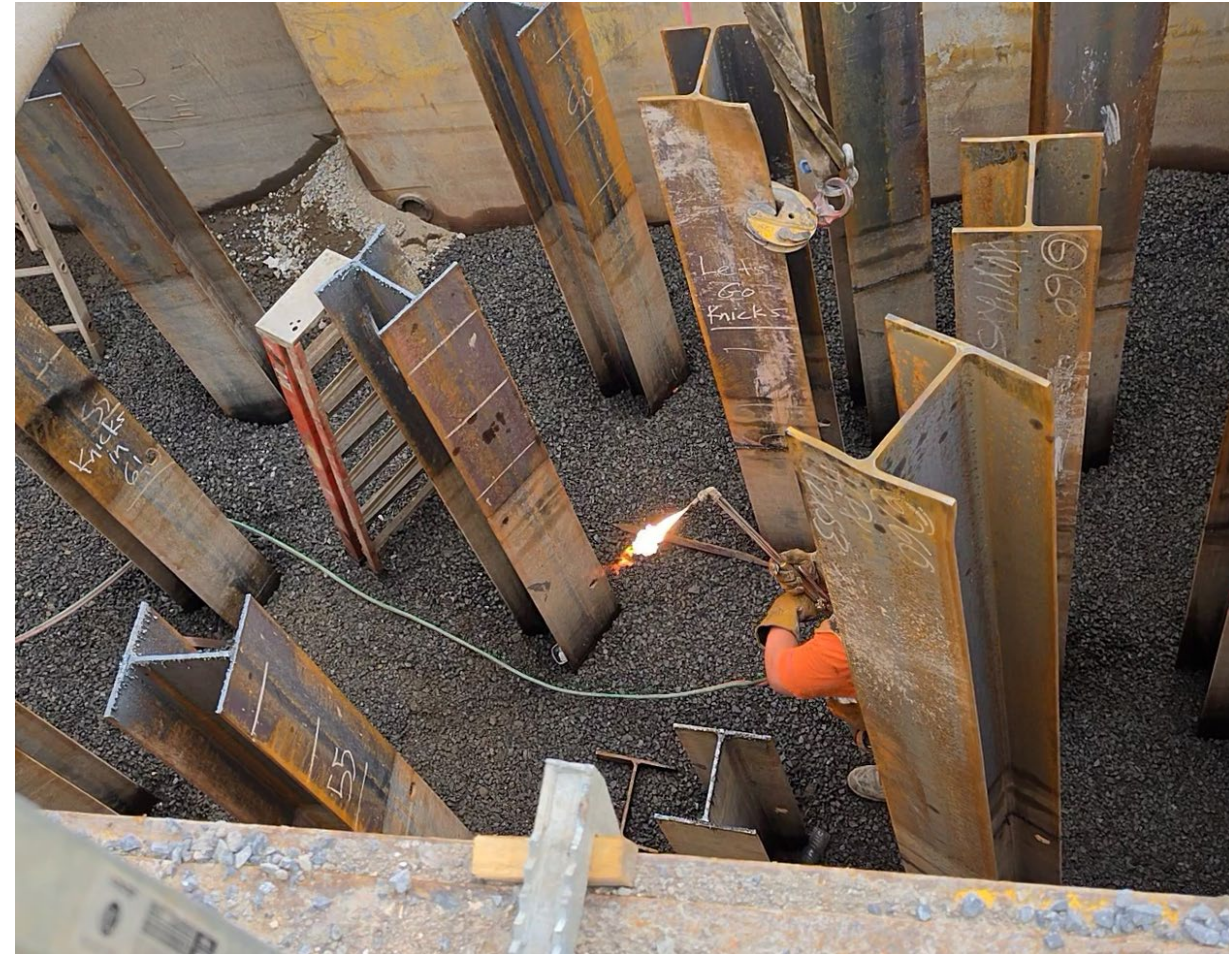

H-piles for sewer support near track area – June 2026

PA1 | Construction Photos



Forming fence and curb line for Field 4 – June 2026



Parks M&O building near Field 7 – June 2026

PA1 | Construction Photos



Sod installation near tennis courts – June 2026



Tree installation near tennis courts and esplanade– June 2026

PA1 | Construction Photos



Tree installation near amphitheater– June 2026



Shrub installation near Parks maintenance area – June 2026

PA1 | What We've Heard

Spring Planting:

- Includes areas surrounding tennis courts, esplanade planter near Pier 42, and areas around Parks maintenance building
- Plantings include both new plants and warranty replacement plants

Public Restroom Building

- ESCR Community Engagement received one construction-related inquiry, which we forwarded to the PRB team
- Per PRB team, construction began earlier this month and is anticipated to complete by end of year

Parallel Conveyance

PC | Construction Activities

ALL WORK IS SUBJECT TO CHANGE

Location 1 – Jackson St. & Corlears Hook Park (Water St. and South St. *complete*)

- Sewer installation

Location 2 – Lewis St. & Delancey St. S

- Sewer installation *complete*

Location 3 – Baruch Dr. & Delancey St. N

- Sewer installation



Location 4 – E Houston St. & Columbia St.

- Sewer installation

Location 5 – Avenue C & E 18th

- Water main
- Sewer installation

Work in Location 6
expected to increase
this summer


Location 6 – Avenue C, E 20th to E 23rd

- Utility relocation
- Test pits

PC | Work in Corlears Hook Park

ALL WORK IS SUBJECT TO CHANGE


Test pits and subsurface investigations	✓
Utility work	Coordination ongoing, to be scheduled
PC sewer installation	
Water main installation	
Final restoration Including Playground and Turf Area	Anticipated to begin by end of year

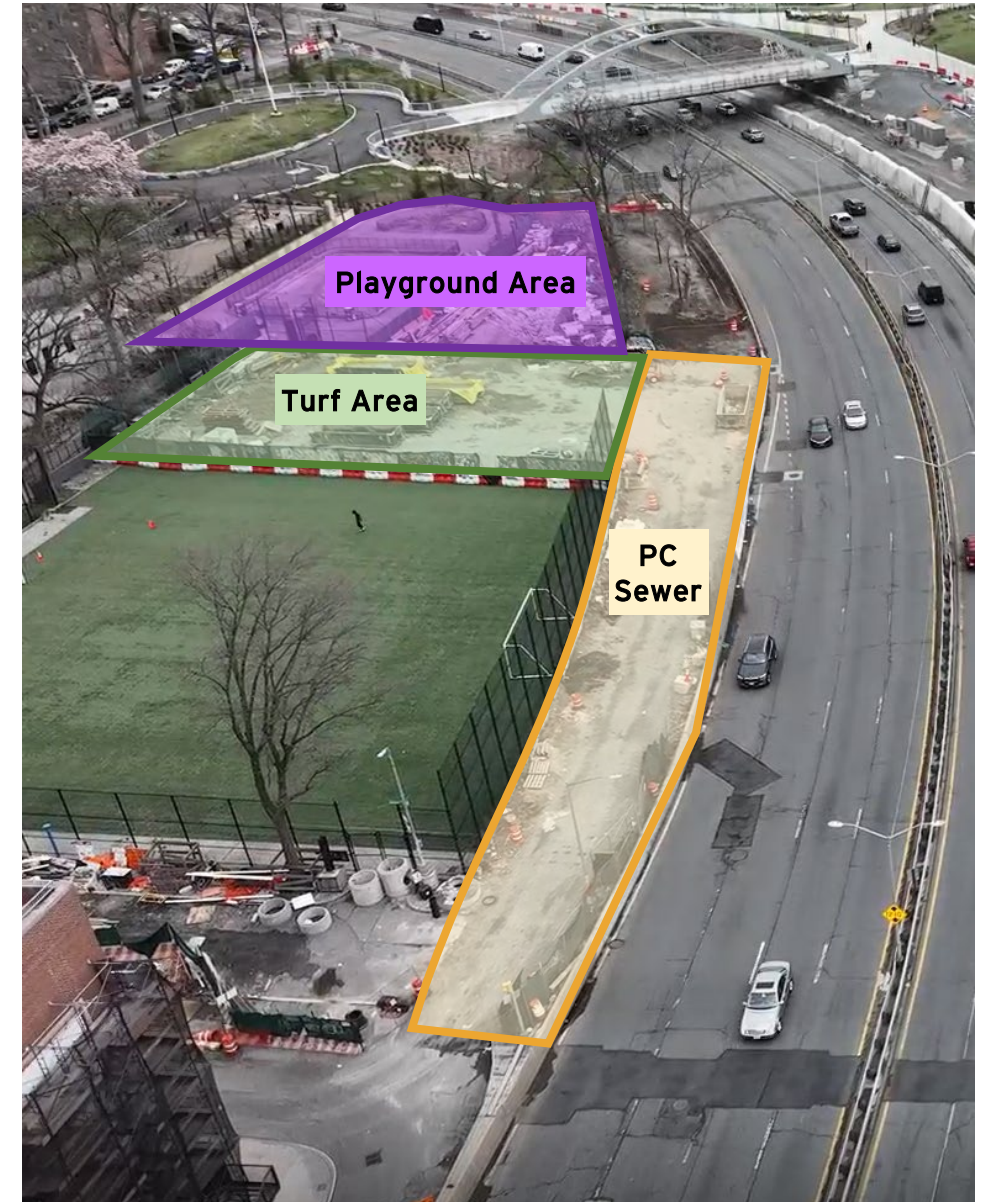

PC | Work in Vicinity of Williamsburg Bridge

ALL WORK IS SUBJECT TO CHANGE

	Delancey Street South & Lewis Street	Delancey Street North & Baruch Drive
Test pits and subsurface investigations	✓	✓
Utility work	✓	✓
Water main installation	✓	To be scheduled after PC sewer
PC sewer installation	✓	In progress Completion anticipated mid-July
Final restoration	To be scheduled at a future date	To be scheduled at a future date

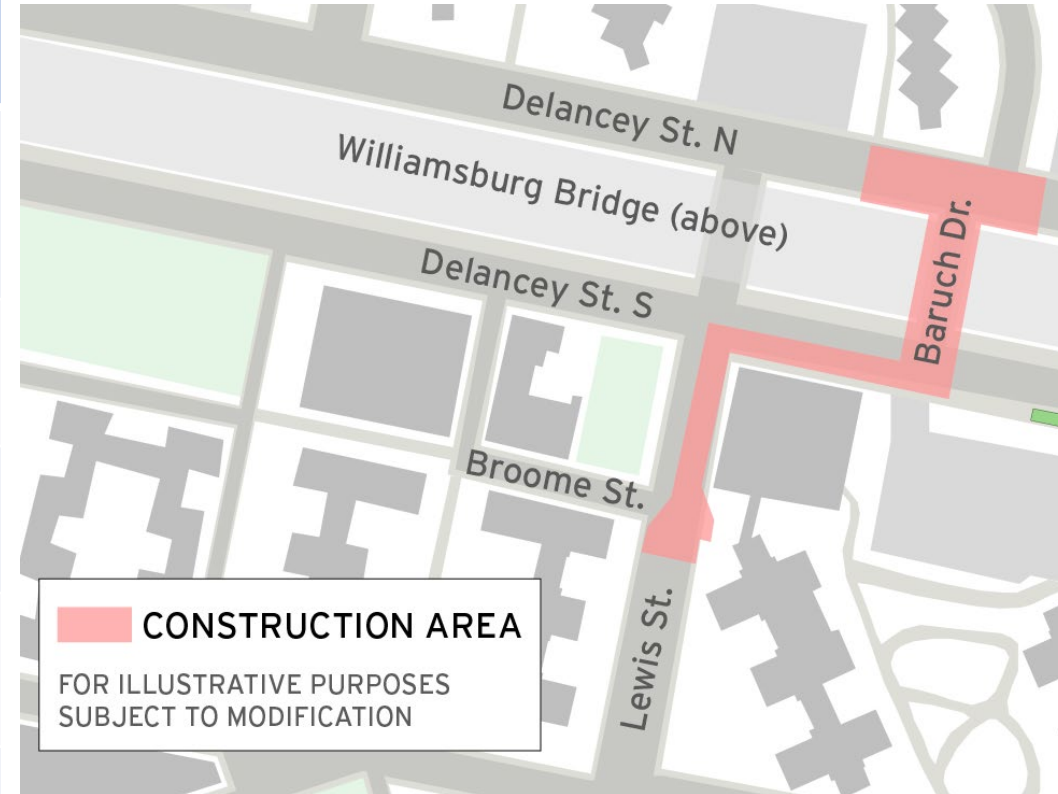

PC | Work at E. Houston St. and Columbia St.

ALL WORK IS SUBJECT TO CHANGE

Test pits and subsurface investigations	✓
Utility work	✓
PC sewer installation	In progress Completion anticipated 6-8 weeks
Final restoration	To be scheduled at a future date




PC | Construction Photos



Construction of deep drop manhole at Delancey St. N and Baruch Drive – May 2026



Installation of precast riser into deep drop manhole at Delancey St. N and Baruch Drive – May 2026

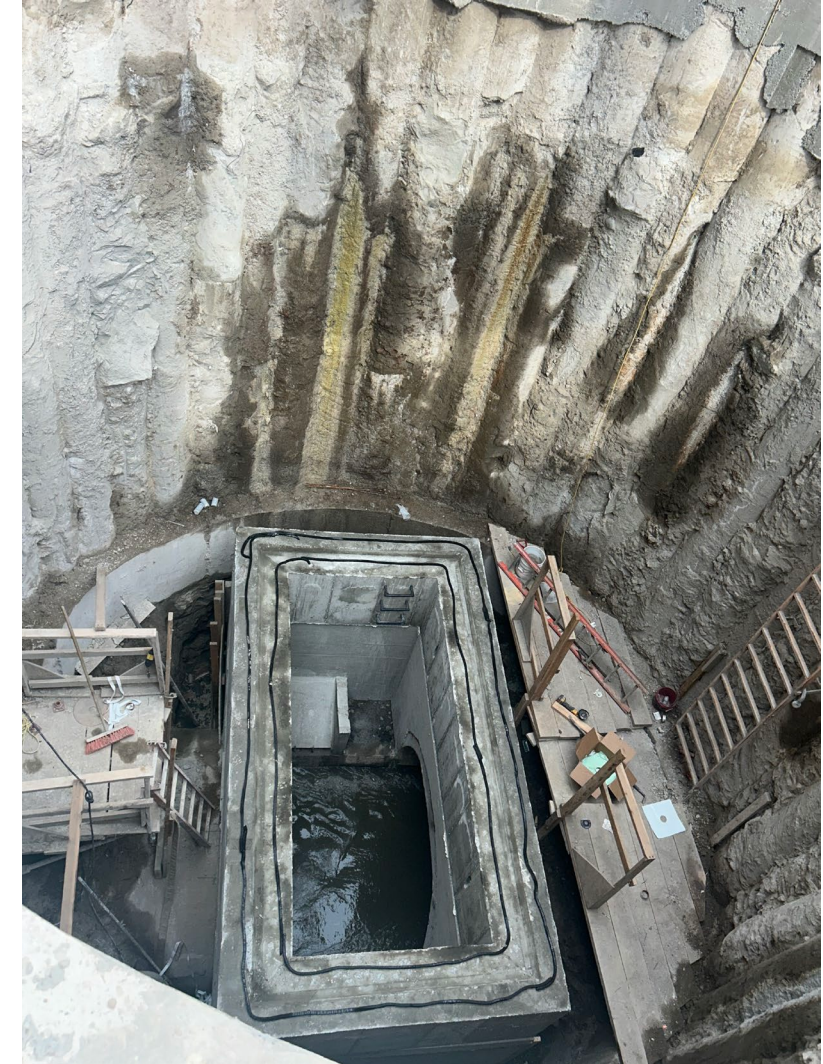

Construction of deep drop manhole around live sewer at Delancey St. N and Baruch Drive – May 2026

ESCR Resources

Project Area 1:

- Vanessa Gomez #(347) 628-8724
- Pauline Chan #(929) 717-9015
- Email: ESCRCCL1@ddccr.com

Parallel Conveyance:


- Tannia Wokoun #(914) 313-6863
- Email: sandrespc.ccl@gmail.com

ESCR Inquiry Tool: nyc.gov/escr/contact

Recent Presentations: <https://on.nyc.gov/3DvPJs2>



Contact Us

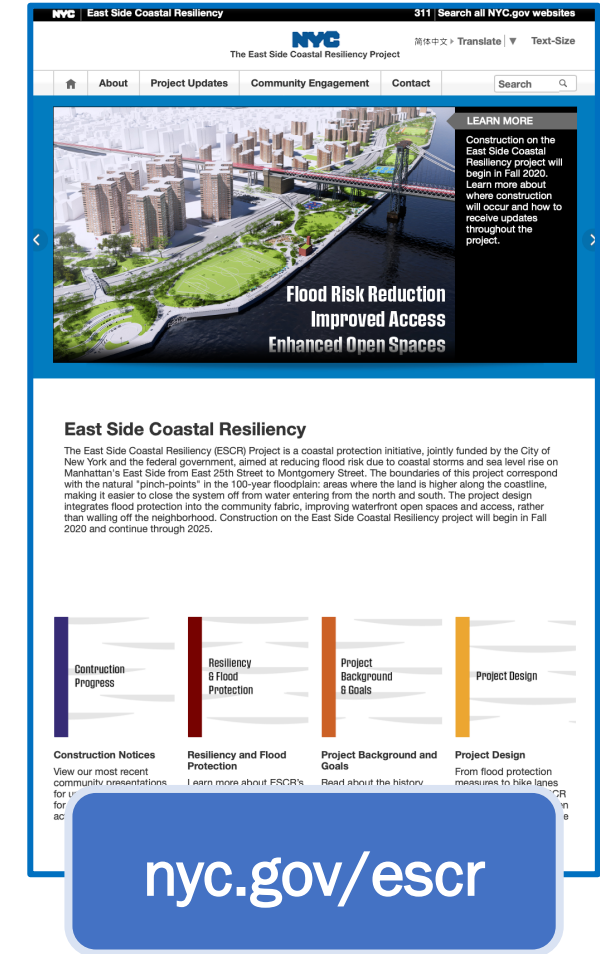

Questions?
