

COMMUNITY ADVISORY GROUP (CAG)

Meeting #72

ESCR FOCUS AREA TOPICS

**CONSTRUCTION
PROGRESS/
APPROACH**

ENVIRONMENT

**ACCESS/
SIGNAGE/
SAFETY**

**PARK
AMENITIES**

**HIRING
COMPLIANCE**

**PROJECT
INFORMATION
DELIVERY**

**COMMUNITY
PROGRAMMING &
COORDINATION**

QUESTIONS?



OVERVIEW

- **Overview of Contracts**
 - **PA2 Construction Progress**
 - **PA1 Construction Activities**
 - **Compost Facility Update**
 - **PA1 What We've Heard**
 - **Targeted Outreach for Upcoming Work**
 - **Call for Art**
 - **PA1 Environmental Reporting**
 - **PC Construction Activities**
- **Upcoming Meetings**

HIRING COMPLIANCE

Employment and Training Fair

SAVE
THE
DATE!


Tuesday, September 22, 2026
4:00pm to 6:00pm

- 213 Stanton Street
New York, NY 10002
- Hosted by ESCR team, in collaboration with Our lady of Sorrows Church
- Prepare and connect with returning workforce partners and community organizations to learn about available employment opportunities.
- Please keep an eye on [our website](#) for registration details.



June 2026 Work With Us Quarterly Employment and Training Fair

Project Area Overview

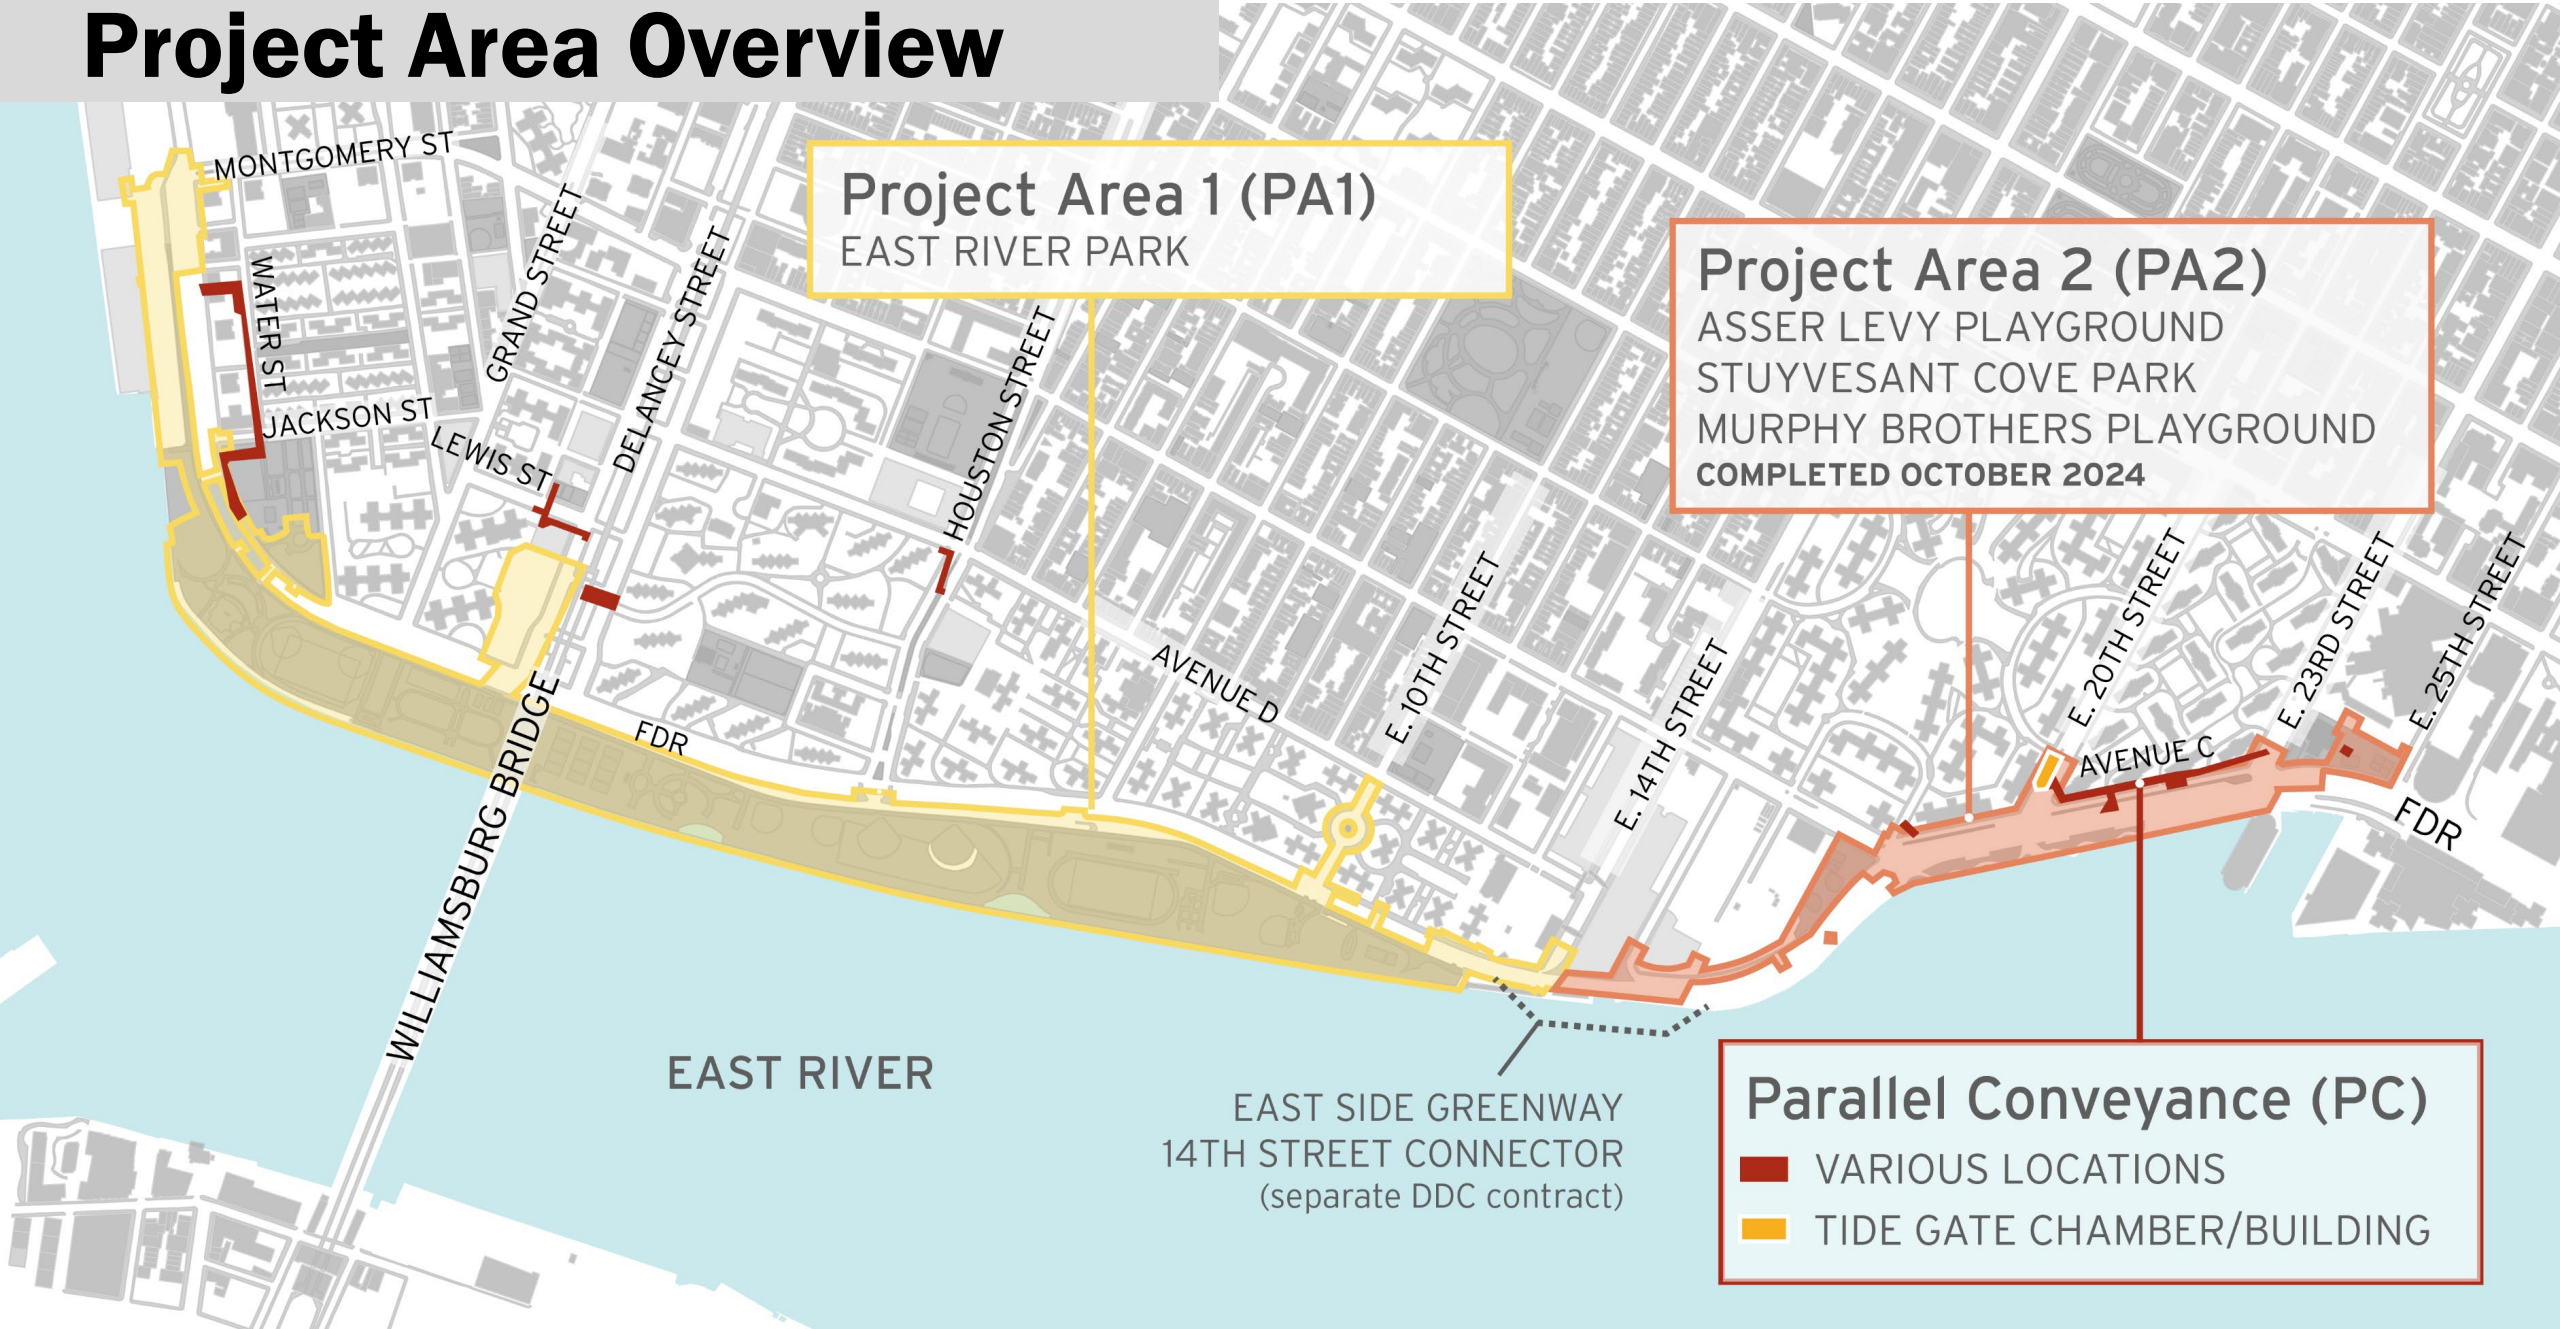

**CONSTRUCTION
PROGRESS/
APPROACH**

PA2 | Construction Progress

- Punch list items throughout
- Asser Levy Playground – **OPEN!**
- Stuyvesant Cove Park – **OPEN!**
- Murphy Brothers Playground - **OPEN!**



Punch list work ongoing in Stuyvesant Cove Park – August 2026




**CONSTRUCTION
PROGRESS/
APPROACH**

PA1 | Construction Progress

PA1 | Construction Activities

ALL WORK IS SUBJECT TO CHANGE

1. Floodwall and floodgate operations.
Construction of Parks maintenance area.
Excavation and clean fill installation.
2. Construction of Parks maintenance & tennis buildings.
Utility and water main work.
3. Esplanade reconstruction, E. Houston Street retaining wall activities.
Clean fill installation.
4. Deep sewer work, floodwall construction, and excavation.
Construction of Parks maintenance & track buildings.
5. E. 10th Street bridge: pile installation.
Preparation for E. 13th Street floodwall construction.
6. Phase 1 amenities **OPEN**.
Punch list items, including Delancey Street & Corlears Hook bridge work.
7. Ongoing partial FDR lane closures at various locations for bridge & floodwall work.

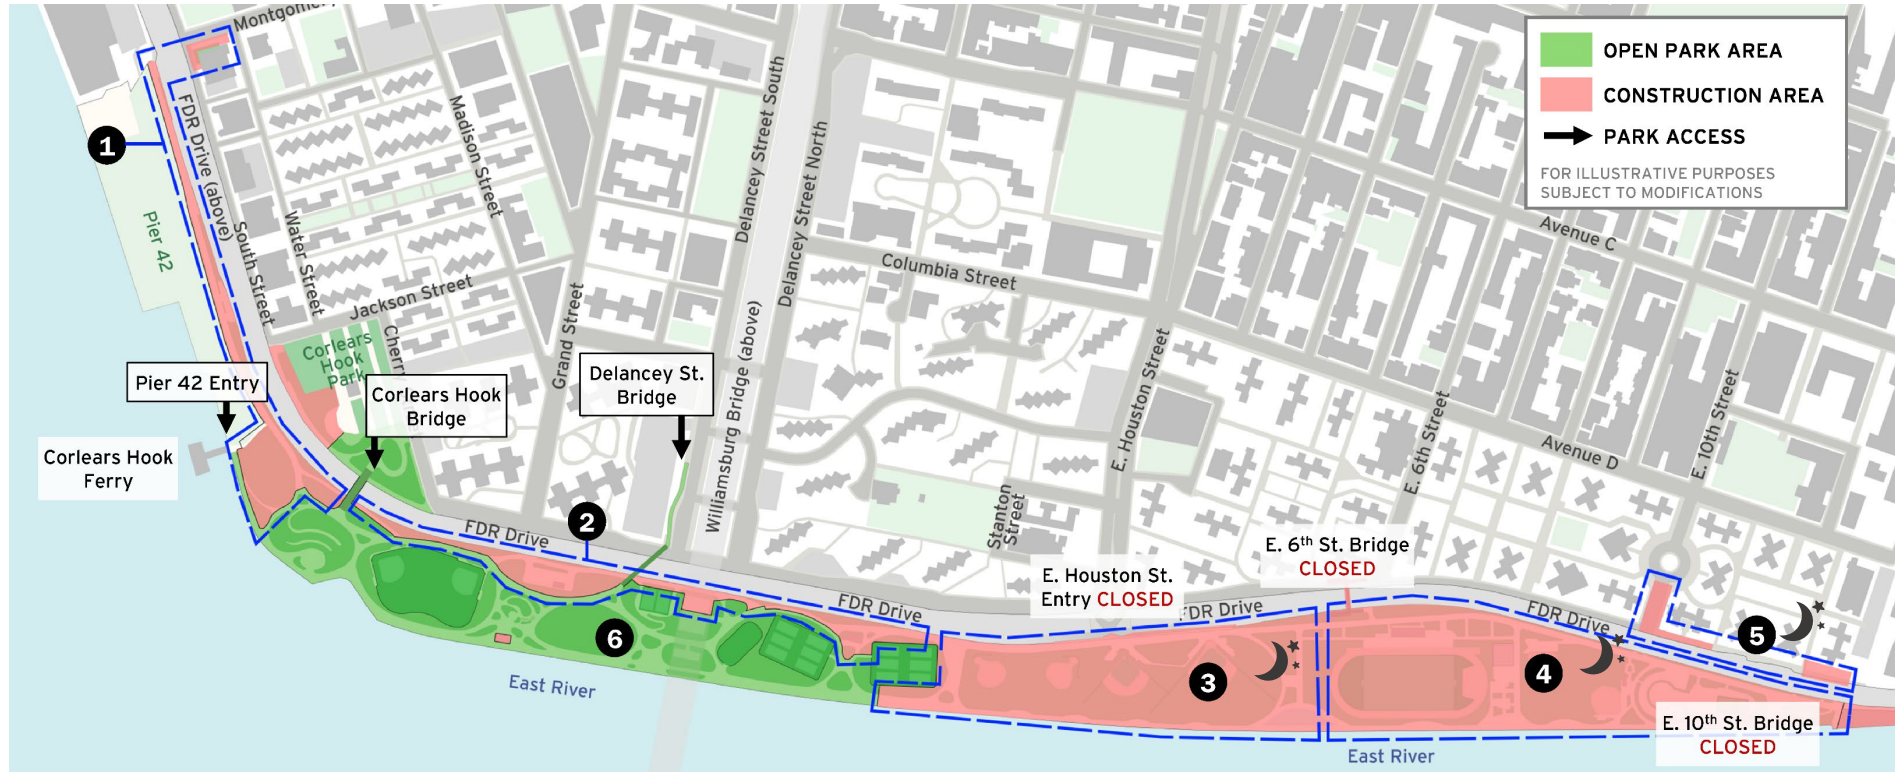

★ INDICATES NIGHT WORK SHIFTS

Weekly Bulletins & Advisories are issued with construction activities.

Saturday work is anticipated for some work operations as indicated.

PA1 | E. 10th St. Bridge Construction

ALL WORK IS SUBJECT TO CHANGE




Similar structures already installed and open at Delancey Street South and Corlears Hook Park

PA1 | E. 10th St. Bridge Construction


ALL WORK IS SUBJECT TO CHANGE

- Construction phasing (approx. 12-14 months total):
 1. Work and staging area mobilization *complete*
 2. Daytime installation of ramp and abutment piles
 - Biggest noise/vibration impact to residents
 - **Pile installation hours: 7am to 6pm**
 - **Anticipated to continue into early October.**
 - Please see [July 2026 CAG](#) for more information on pile installation methods and noise mitigation strategies.
 3. Assembly of bridge on E. 10th Street (~2 months)
 4. Bridge placement (1 night)
 5. Construction of ramps (~6-7 months)

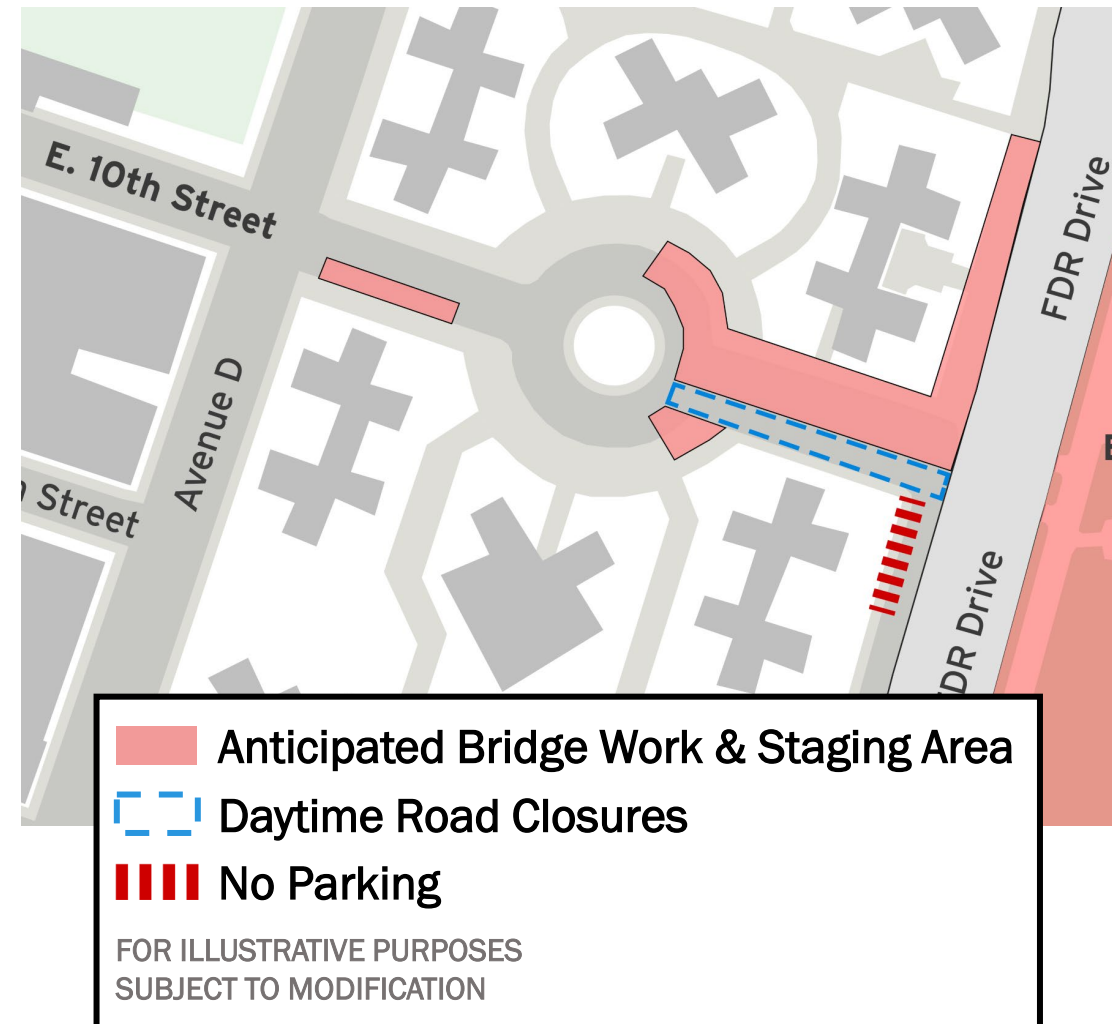

PA1 | E. 10th St. Bridge Construction

ALL WORK IS SUBJECT TO CHANGE

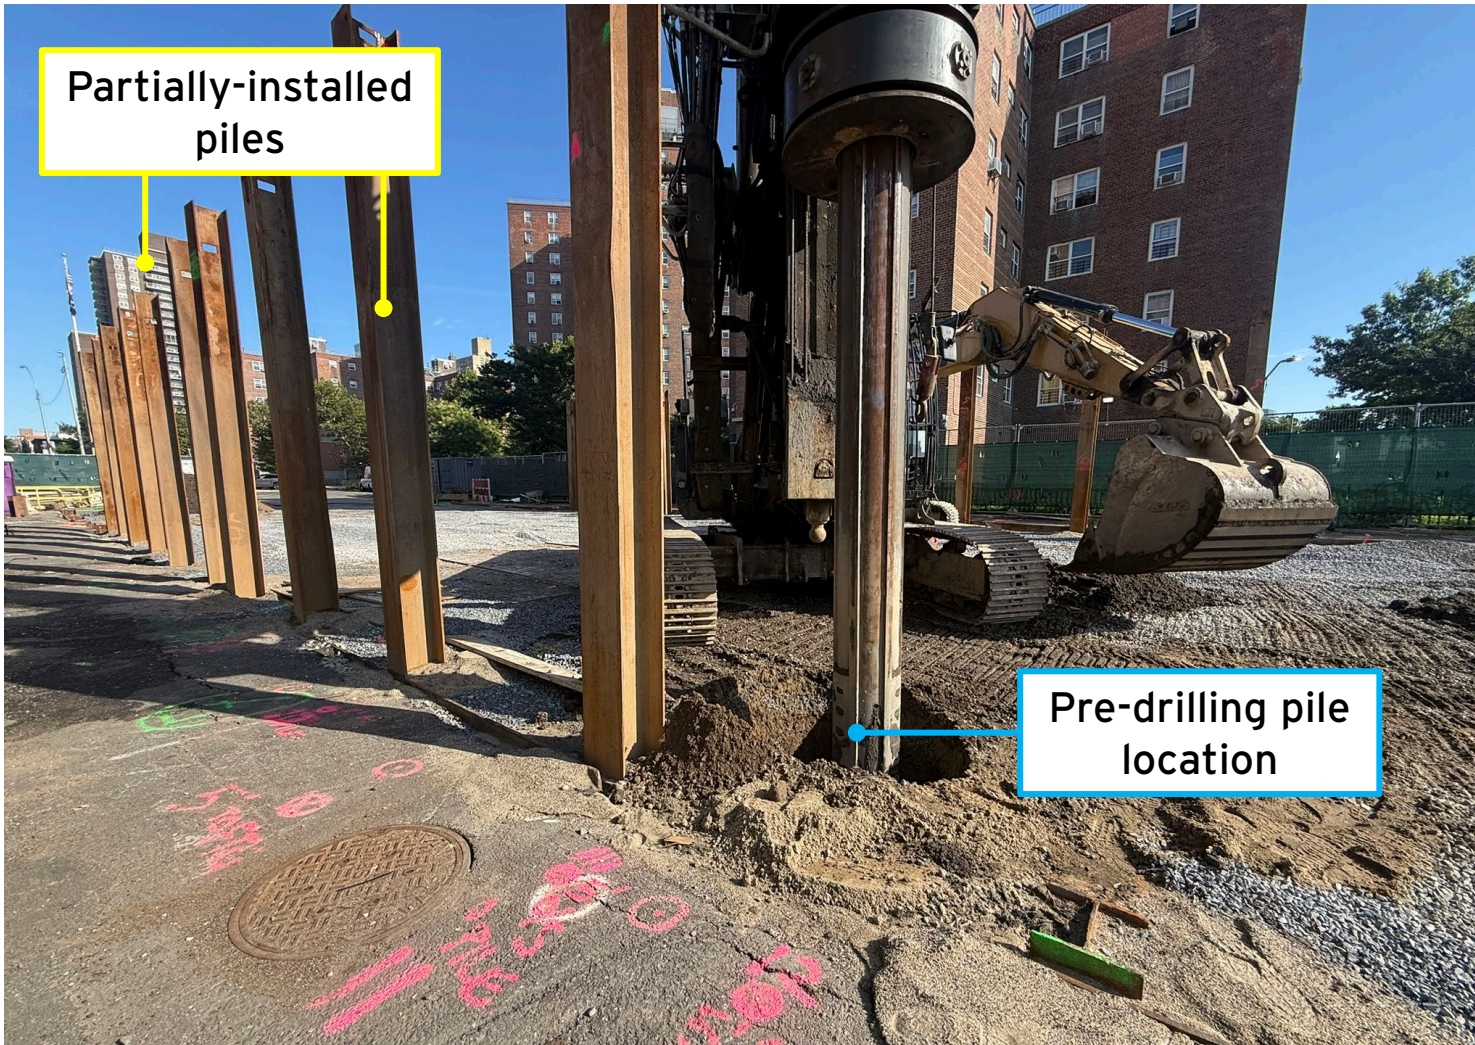

E. 10th Street bridge pile installation – August 2026



Noise mitigation blankets installed adjacent to bridge work area – August 2026

PA1 | E. 13th St. Flood Protection Construction


ALL WORK IS SUBJECT TO CHANGE



PA1 | E. 13th St. Flood Protection Construction

ALL WORK IS SUBJECT TO CHANGE

- Pile installation to be installed across and parallel to the FDR Drive to support flood protection infrastructure.
- Unfortunately, this work is required by DOT to be performed at night (roughly 10pm to 6am, dependent on day of week)
- Anticipated to begin mid- to late-September, ongoing for approx. two months
 - Please see [July 2026 CAG](#) for more information on pile installation methods and noise mitigation strategies.
- When dates are confirmed, we will provide as much advance notice as possible via formal advisories and at nyc.gov/escr/nightwork

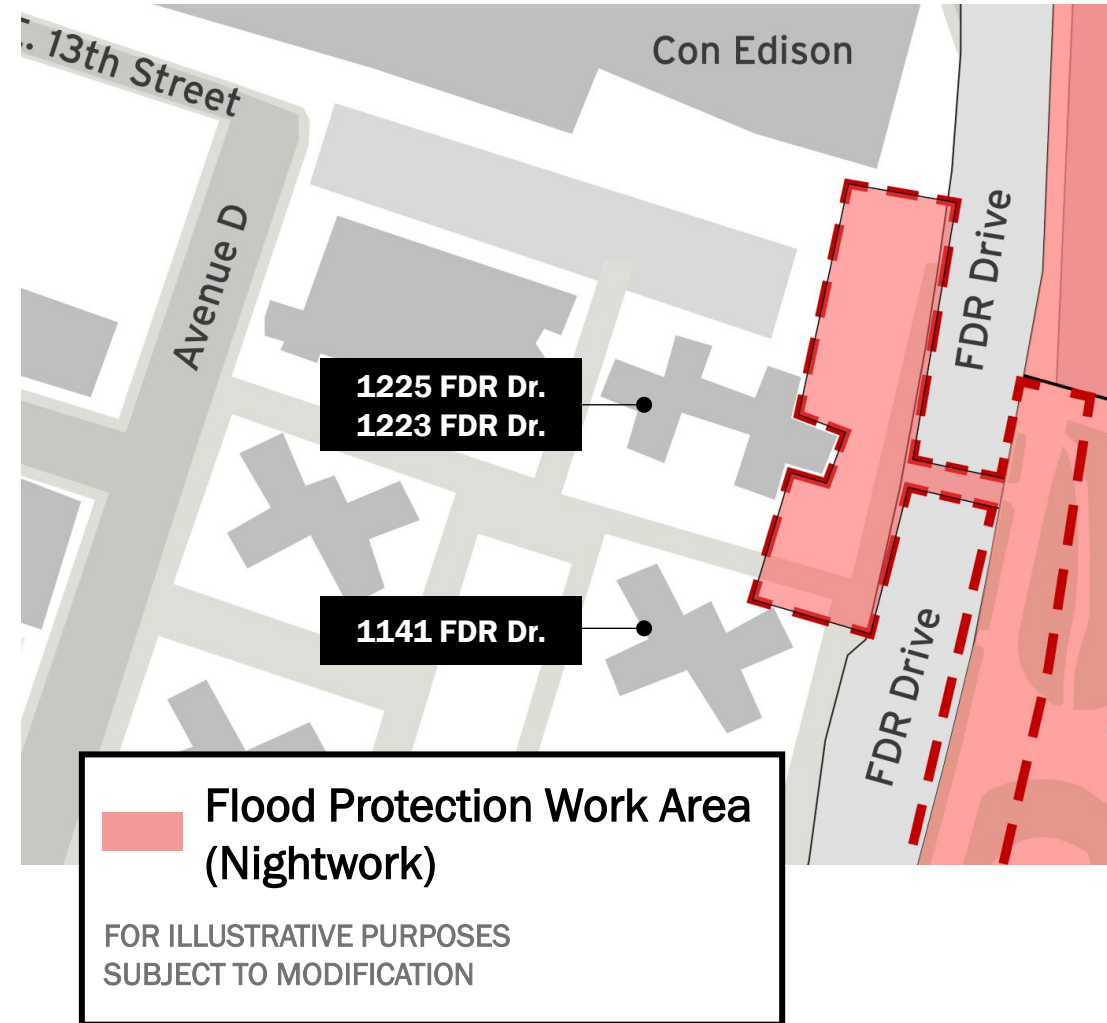

PA1 | Construction Photos

PA1 | Construction Photos

ALL WORK IS SUBJECT TO CHANGE



New portion of esplanade opened adjacent to north tennis courts – August 2026




New pathway opened near Corlears Hook Ferry Terminal – August 2026

PA1 | Construction Photos

ALL WORK IS SUBJECT TO CHANGE



Floodwall construction and curb work south of Corlears Hook – August 2026

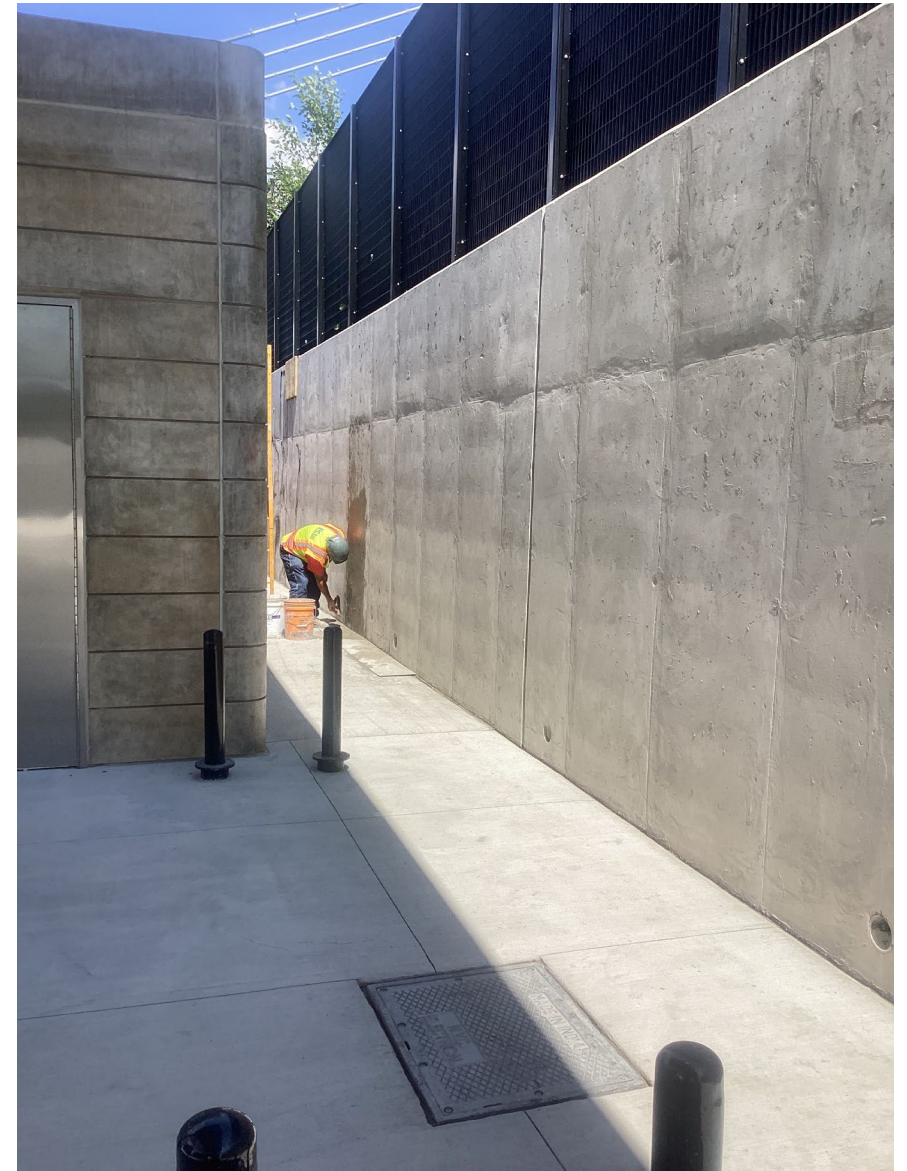

Graffiti removal at Parks maintenance area – August 2026

PA1 | Construction Photos

ALL WORK IS SUBJECT TO CHANGE



Performing site maintenance near E. 10th Street bridge construction – August 2026




Bridge pile splicing (welding) – August 2026

PA1 | Construction Photos

ALL WORK IS SUBJECT TO CHANGE



Northern embayment construction – August 2026

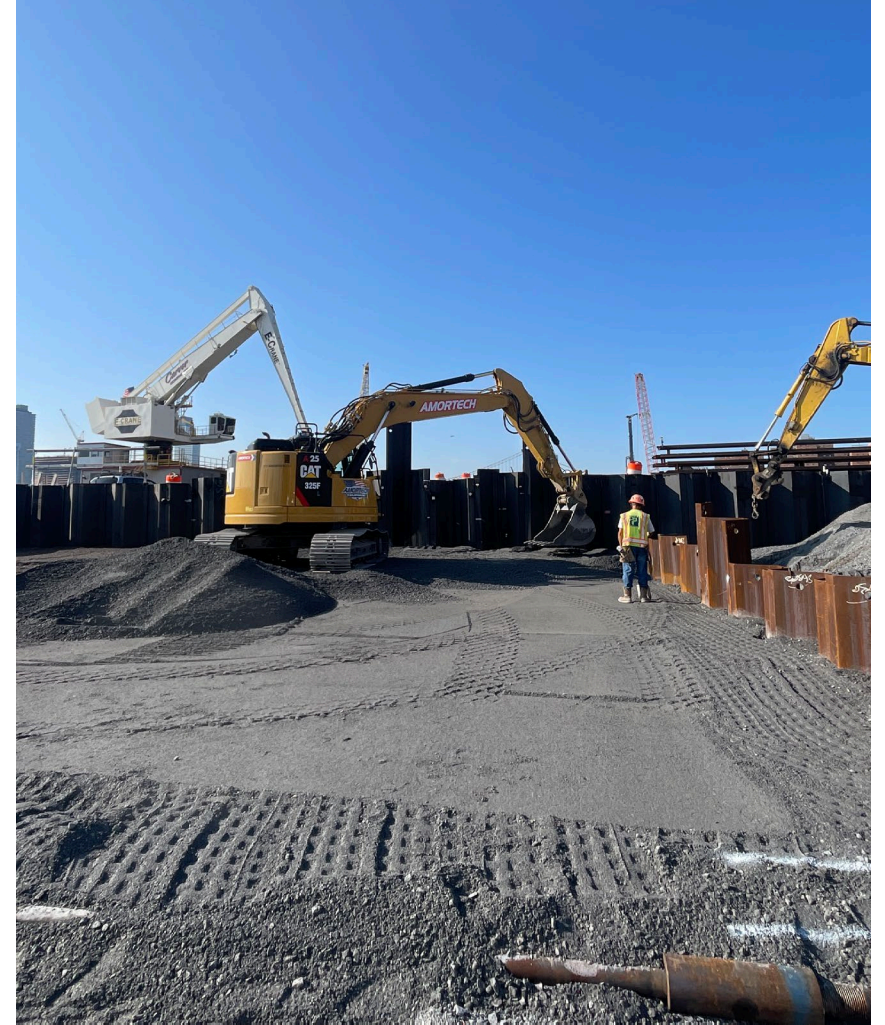

Clean fill installation for future sports fields – August 2026

PA1 | Compost Facility Update

ALL WORK IS SUBJECT TO CHANGE

- The City has experienced procurement-related challenges associated with utilizing the Change Order process for this project, given the scale and cost estimates of the proposed facility.
- Therefore, DDC is turning to the competitive bidding process.
- The bid is anticipated to go out later this year, which would point to an anticipated construction completion date of late 2028 at earliest.
- This is the most viable path to keep the project moving forward.
- LESEC has been informed of this update, and we will continue to keep our lines of communication with them open as the process moves forward.
- We will present this information again at the 9/17 CB3 Parks Committee Meeting.



Compost Facility Rendering for PDC Submission

PA1 | What We've Heard: Riis

East River Park Anchor:

- Anchor was a replica intended to acknowledge the neighborhood's waterfront history.
- Parks Department relocated the anchor to Dyckman Marina.
- We shared residents' request to have the anchor returned to East River Park with the Parks Department.


E. 10th Street Road and Pedestrian Conditions During Construction:

- We are looking into existing conditions with the project team and will provide updates as soon as possible.
- Team is assessing adding new signage as requested by Riis TA.
- Ongoing communications with Contractor on appropriate parking areas near E. 10th St.

PA1 | What We've Heard: Shared Use Path

July CAG: request for width of shared use path between Pier 42 and Parks M&O facility.


- For illustrative purposes only, subject to modification. Figures shown are approximate.

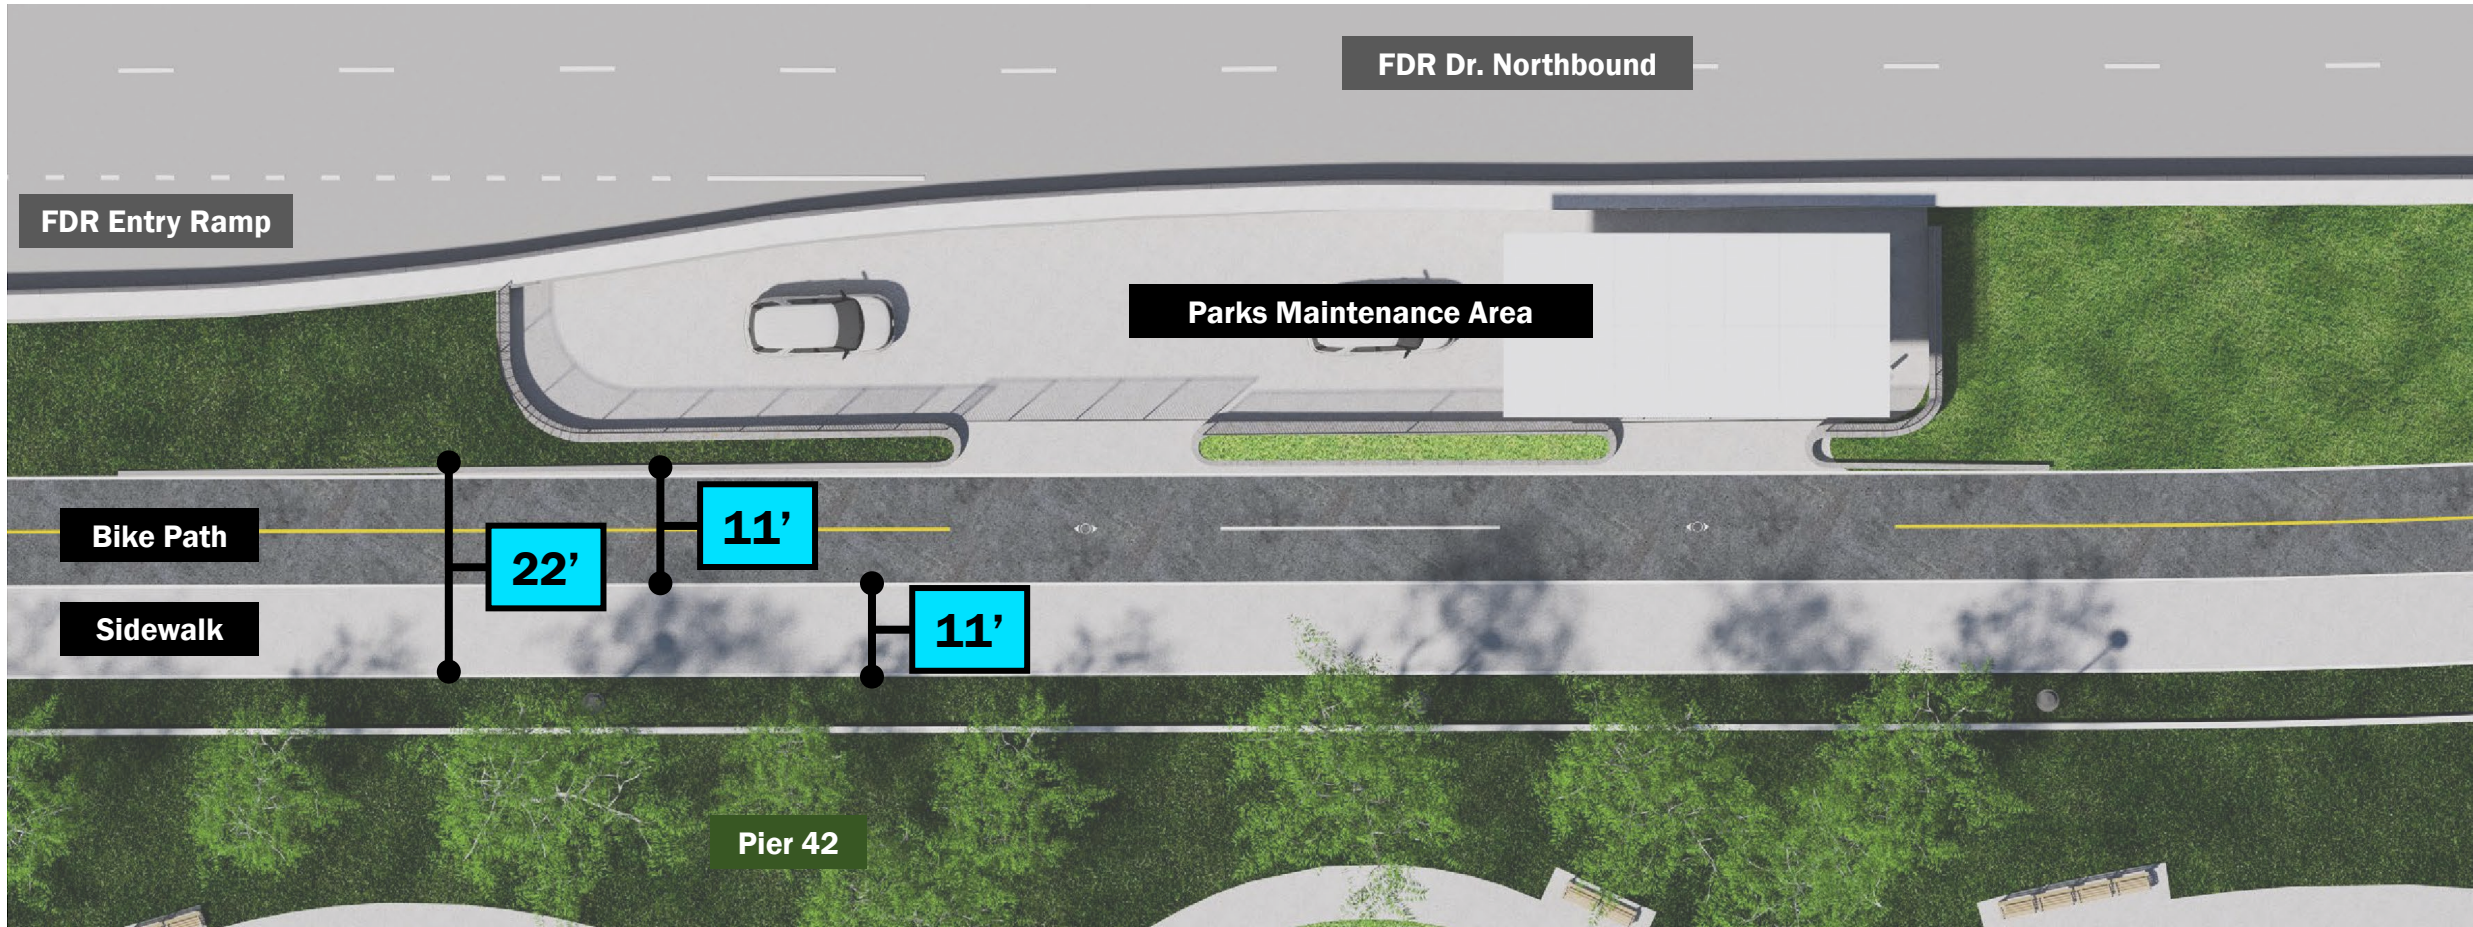

PA1 | What We've Heard: Park Elevations

July CAG: request for approximate elevations in East River Park, north of E. Houston Street..

- For illustrative purposes only, subject to modification. Figures shown are approximate increase in elevation from prior grade.
- This information was previously provided to the CAG via email in February 2025.

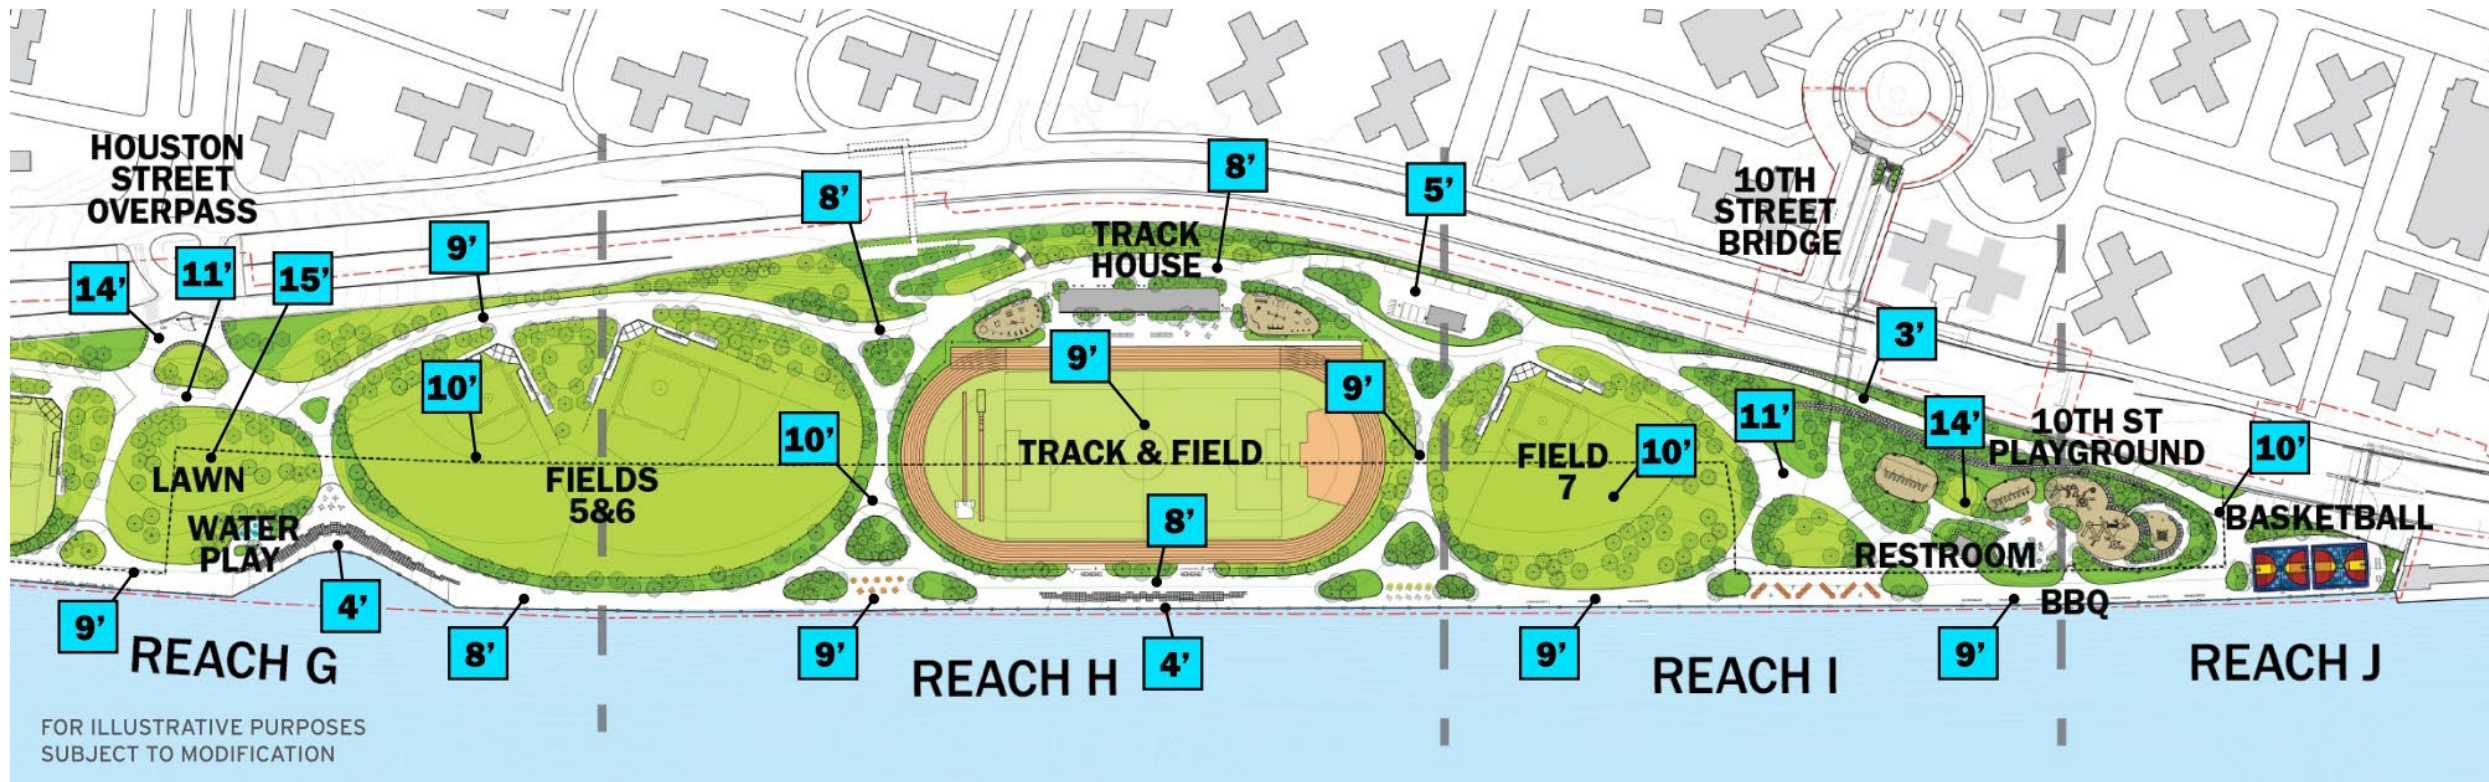


A green circle logo containing the text "PROJECT INFORMATION DELIVERY" in white, bold, uppercase letters.

**PROJECT
INFORMATION
DELIVERY**

Targeted Outreach for Upcoming Work

PA1 | Targeted Outreach for Upcoming Work

- Engagement team will be at August 29 Family Day and September 8 TA Meeting.
- Virtual meetings for Riis residents will be held on the **second Thursday of every month at 11am** until further notice, beginning September 10.
- Virtual Riis meeting recordings (including Aug. 20th presentation), slide translations, and updates are posted to our dedicated Riis webpage: nyc.gov/escr/nightwork
 - All community presentations can be found here: <https://www.nyc.gov/site/escr/project-updates/presentations.page>
- The Community Engagement team also frequently flyers in the area, including on Pantry Days.

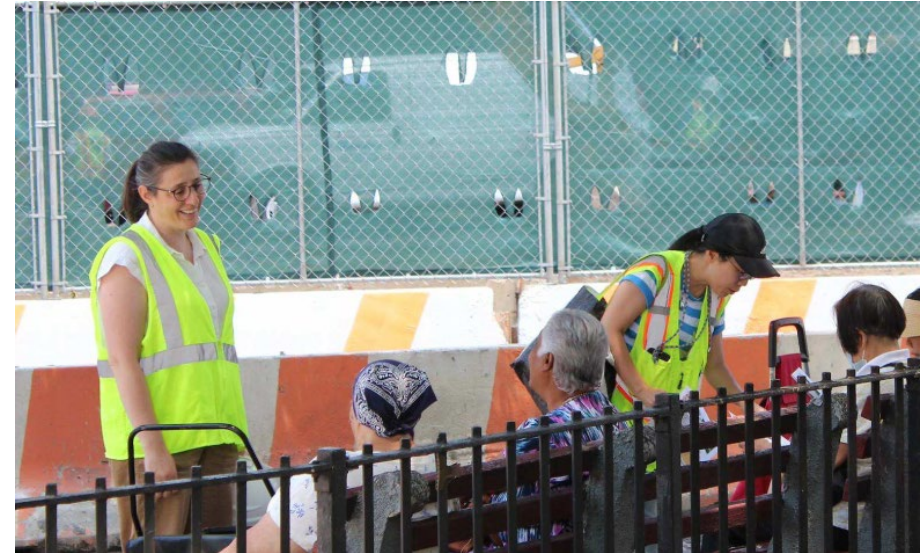

Flying at Riis, July 2026



Community Event at Riis, August 2026

COMMUNITY
PROGRAMMING &
COORDINATION

Call for Art 2026



on.nyc.gov/4egUBPI

EAST SIDE COASTAL RESILIENCY

CALL FOR ART

What: Submit your art to be printed on construction fencing near E. 10th Street and the FDR Drive!

Who: Residents and artists of all ages near E. 10th Street and East River Park. Jacob Riis residents encouraged to participate!

How: Submit your artwork with the attached form to drop boxes at the NYCHA Riis Houses Management Office (454 E. 10th St.) or Tompkins Square Library (331 E. 10th St.). You can also email ESCRCCCL1@ddccr.com to arrange pick-up or if you'd like to submit digitally (see page 2). Art will be returned.

When: Submissions due by **Friday, October 16, 2026**. Selected artwork will be displayed along construction fencing in late-2026 / early-2027.

活动目的: 招募艺术将用于装饰位于东10街, 介于D大道和FDR 高速之间周围的施工围挡上!

参与群体: 居住在东10街及东河公园附近、各年龄的居民与艺术家。鼓励Jacob Riis居民一起参与!

提交方式: 请将您的艺术作品附上表格, 放置位于以下地点的收集箱内: NYCHA Riis Houses 管理办公室 (454 E. 10th St.) 或 Tompkins Square 图书馆 (331 E. 10th St.)。或者, 您可以以电子邮件至 ESCRCCCL1@ddccr.com 安排收取作品, 或提交电子版作品 (详见第2页)。所有艺术作品均会归还。

提交截止日期: 2026年10月16日 (星期五)。选定的艺术作品将于 2026 年底至 2027 年初沿着施工围挡展示。

Qué: Convocatoria artística para decorar las cercas de construcción cercanas a E. 10th St entre Avenue D y FDR Drive.

Quién: Residentes y artistas de todas las edades cerca de E. 10th Street and East River Park. ¡Animamos a los residentes de Jacob Riis a participar!

Cómo: Entregue su propuestas con el formulario adjunto en el buzón ubicado en la oficina de NYCHA Riis Houses (454 E. 10th Street) o en Tompkins Square Library (331 E. 10th St.) (vea el mapa). Alternativamente, puede enviar un correo electrónico a ESCRCCCL1@ddccr.com para organizar la recogida o si desea hacer una entrega digital. El arte se va a devolver a los participantes.

Cuando: Las entregas deben presentarse antes del viernes 16 de Octubre de 2026. Las obras de arte seleccionadas se exhibirán a lo largo de las cercas de construcción a fines de 2026/inicios 2027.

Suggested Themes

What stories, cultures, and identities make NYC's waterfront unique?
What does climate resiliency mean to you?
哪些故事、文化和身份使纽约市的海滨独特?
气候复原力对你来说意味着什么呢?

¿Qué historias, culturas e identidades hacen único el frente de río de la ciudad de Nueva York?
¿Qué significa para ti la resiliencia climática?

Drop-off Location

Tompkins Square Library
331 E. 10th Street

NYCHA Riis Houses Management Office
454 E. 10th Street

Questions? Preguntas? 问题?

Please contact our Community Construction Liaisons (CCL) for project-related inquiries or concerns:
Vanessa Gomez (para mas información llame): 347-628-8724
Pauline Chan (欢迎中文咨询): 929-717-9015
Email: ESCRCCCL1@ddccr.com
Submit an inquiry: nyc.gov/e-sc/contact

NYC Department of Design and Construction
NYC Parks
NYC Environmental Protection
NYC DOT


- Invitation for community members to submit visual artwork to be printed on construction fencing, with an emphasis towards residents of NYCHA Riis.
- Suggested Themes:
 - What stories, cultures, and identities make NYC's waterfront unique?
 - What does climate resiliency mean to you?
- Email ESCRCCCL1@ddccr.com to make digital submission or arrange a pick-up; or submit at a drop-off location
- Flyers available in English, Spanish, and Chinese
- Deadline for submissions: October 16, 2026



ENVIRONMENT

Environmental Reporting Update Air Quality Monitoring (AQM)

PA1 AQM | Monitoring Locations

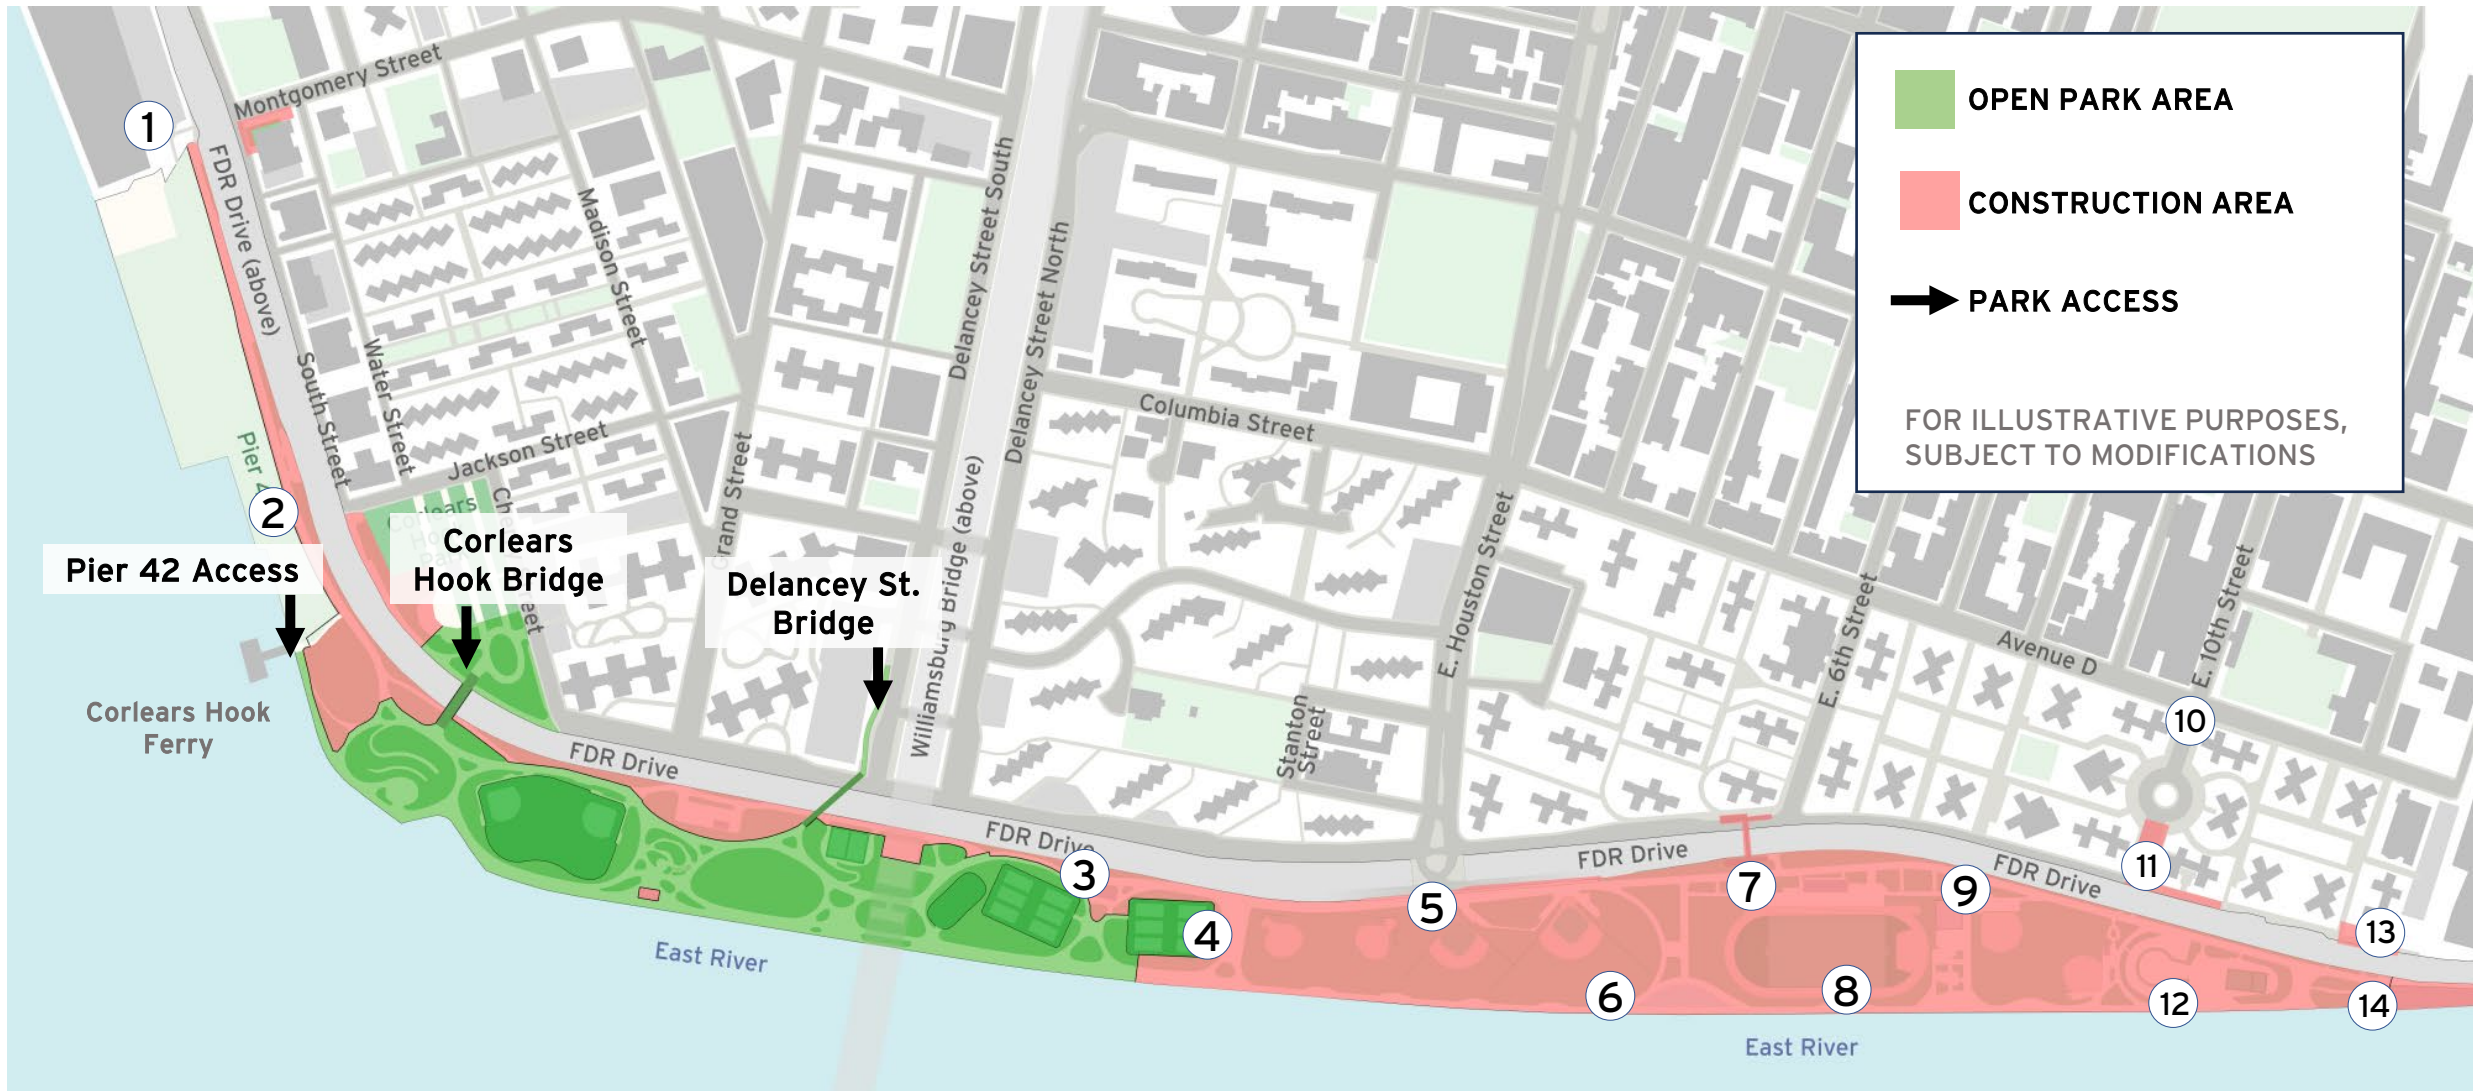

PA1 AQM | July 2026 Update

The PM daily value (24-hour TWA) did surpass the PEL for this month. El valor diario de PM (promedio ponderado de tiempo de 24 horas) no superó el límite de exposición permisible (PEL) para este mes.
这个月的颗粒物日值（24小时加权平均值）没有超过允许的暴露标准。 PM = Particulate Matter / Materia Particular / 颗粒物

Location <i>Ubicación</i> 位置	PM Size <i>PM Tamaño</i> 颗粒物尺寸	Date / Fecha / 日期 <i>BOLD = net exceedances 加粗 = 净超标</i> <i>DESTACADO= superaciones netas</i>	Alert Duration (<i>minutes</i>) <i>Duración de Aviso (minutos)</i> 预警持续时间（分钟）	Cause <i>Causa</i> 原因	Mitigation <i>Mitigación</i> 减缓措施
Montgomery Street to Delancey Street (AQM-6, AQM-CHR)	PM 2.5	7/11 7/15, 7/16, 7/17 and 7/18	11 334 to 1,076	•Offsite Activities •Canadian Wildfire Smoke (NYSDEC Air Quality Advisory Alerts)	•None •None
	PM 10	N/A	N/A	•N/A	•N/A
Delancey Street to East Houston Street (AQM-4, AQM-WBN)	PM 2.5	7/15, 7/16, 7/17 and 7/18 7/24 and 7/25	301 to 1,083 1 to 15	•Canadian Wildfire Smoke (NYSDEC Air Quality Advisory Alerts) •Offsite Activities	•None •None
	PM 10	N/A	N/A	•N/A	•N/A
East Houston Street to East 6 th Street (AQM-3, AQM-5)	PM 2.5	7/10, 7/13, 7/24 and 7/25 7/14, 7/15, 7/16, 7/17 and 7/18 7/27	4 to 73 76 to 652 3	•Offsite Activities •Canadian Wildfire Smoke (NYSDEC Air Quality Advisory Alerts) •Construction Activities	•None •None •None (Welding Activities)
	PM 10	7/10, 7/13, 7/24, 7/25 and 7/27 7/14 and 7/16	7 to 55 16 to 75	•Construction Activities •Offsite Activities	•Dust Mitigation •None
East 6 th Street to East 10 th Street (AQM-TH, AQM-THR, AQM-7)	PM 2.5	7/15, 7/16, 7/17 and 7/18 7/2	253 to 746 7	•Canadian Wildfire Smoke (NYSDEC Air Quality Advisory Alerts) •Construction Activities	•None •Dust Mitigation
	PM 10	7/2	4	•Construction Activities	•Dust Mitigation
East 10 th Street to East 14 th Street (AQM-10S, AQM-10SR, AQM-8, AQM-1, AQM-2)	PM 2.5	7/4 7/15, 7/16, 7/17 and 7/18	6 275 to 970	•Offsite Activities •Canadian Wildfire Smoke (NYSDEC Air Quality Advisory Alerts)	•None •None
	PM 10	N/A	N/A	•N/A	•N/A



PC | Construction Progress

PC | Construction Activities

ALL WORK IS SUBJECT TO CHANGE

Location 1 – Jackson St. & Corlears Hook Park (Water St. and South St. *complete*)

- Sewer installation resumed on Jackson Street and Corlears Hook Park/FDR Drive corridor

Location 2 – Lewis St. & Delancey St. S

- Sewer installation *complete*
- Final restoration *complete*

Location 3 – Baruch Dr. & Delancey St. N

- Sewer installation *complete*

Location 4 – E Houston St. & Columbia St.

- Unanticipated utility relocation
- Sewer installation



Location 5 – Avenue C & E 18th
Only weekend work

- Water main
- Sewer installation


Location 6 – Avenue C, E 20th to E 23rd

- Utility relocation

PC | Work in Corlears Hook Park

ALL WORK IS SUBJECT TO CHANGE


Test pits and subsurface investigations	✓
Utility work	Ongoing
PC sewer installation	Resumed, ongoing
Water main installation	To be scheduled
Final restoration*	Anticipated to begin by end of year
*Installation of Playground and Turf Area	To be scheduled

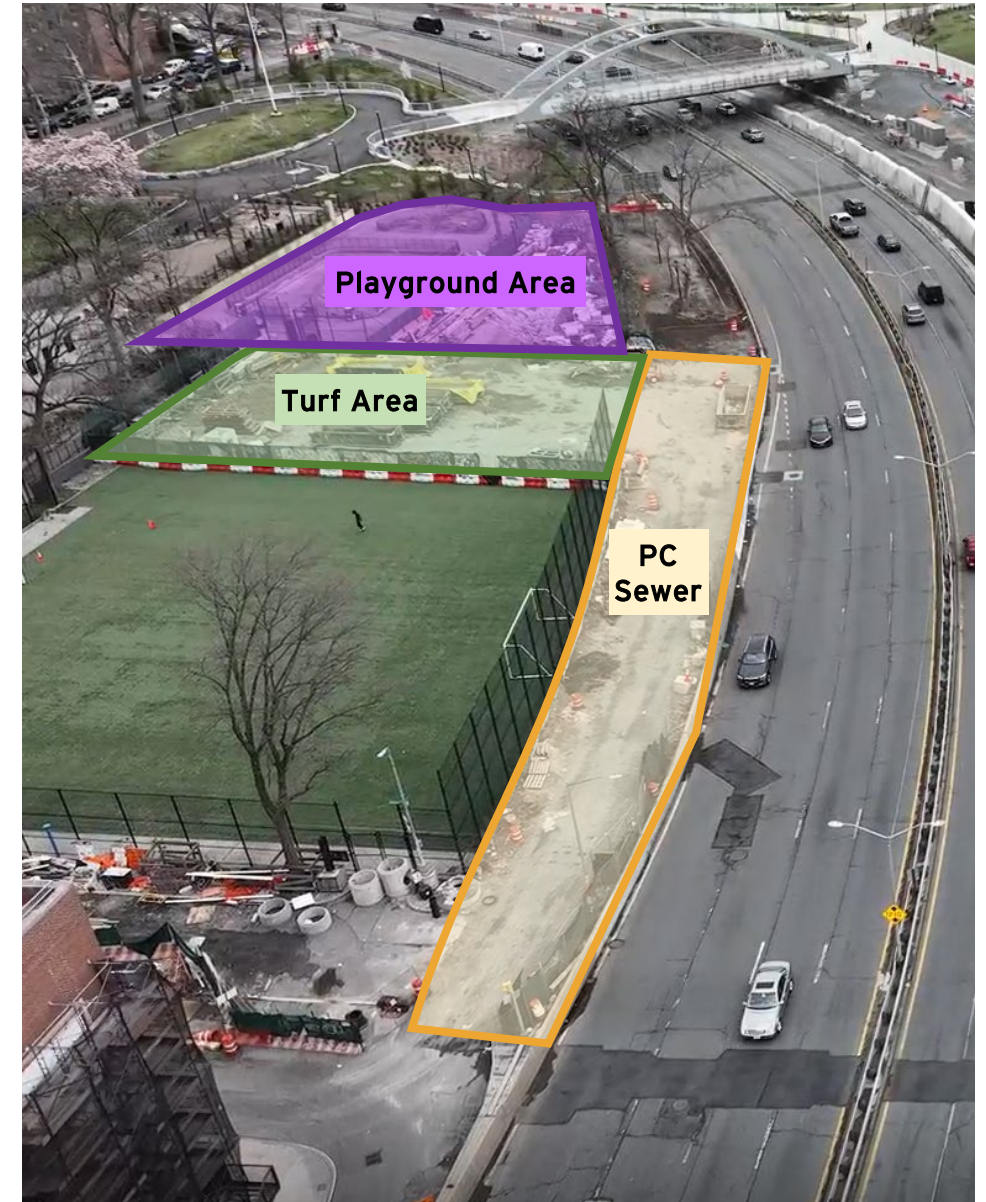

PC | Work in Vicinity of Williamsburg Bridge

ALL WORK IS SUBJECT TO CHANGE

	Delancey Street South & Lewis Street	Delancey Street North & Baruch Drive
Test pits and subsurface investigations	✓	✓
Utility work	✓	✓
Water main installation	✓	✓
PC sewer installation	✓	✓
Final restoration	✓	To be scheduled

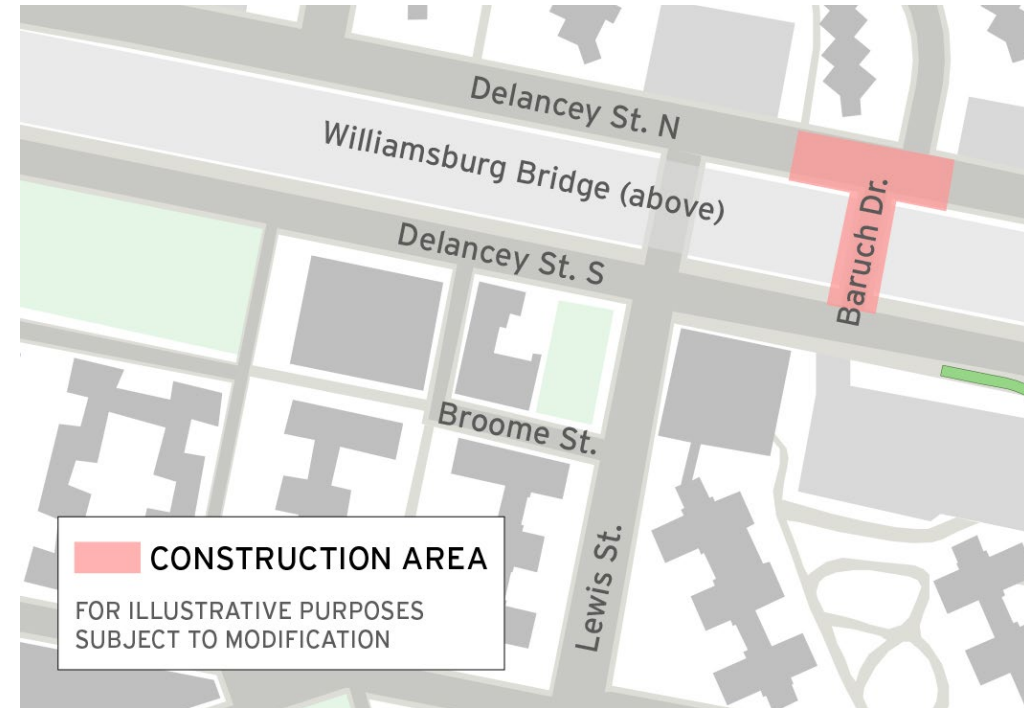

PC | Work at E. Houston St. and Columbia St.

ALL WORK IS SUBJECT TO CHANGE


Test pits and subsurface investigations	✓
Utility work	In progress
PC sewer installation	In progress
Final restoration	To be scheduled



PC | Northernmost Work Areas

ALL WORK IS SUBJECT TO CHANGE

	Ave C & E. 18 th St.	Avenue C, E. 20 th St. to E. 23 rd St.
Test pits and subsurface investigations	In progress	In progress
Utility work	In progress	In progress
Water main installation	Expected soon	To be scheduled
PC sewer installation	To be scheduled	To be scheduled
Final restoration	To be scheduled	To be scheduled

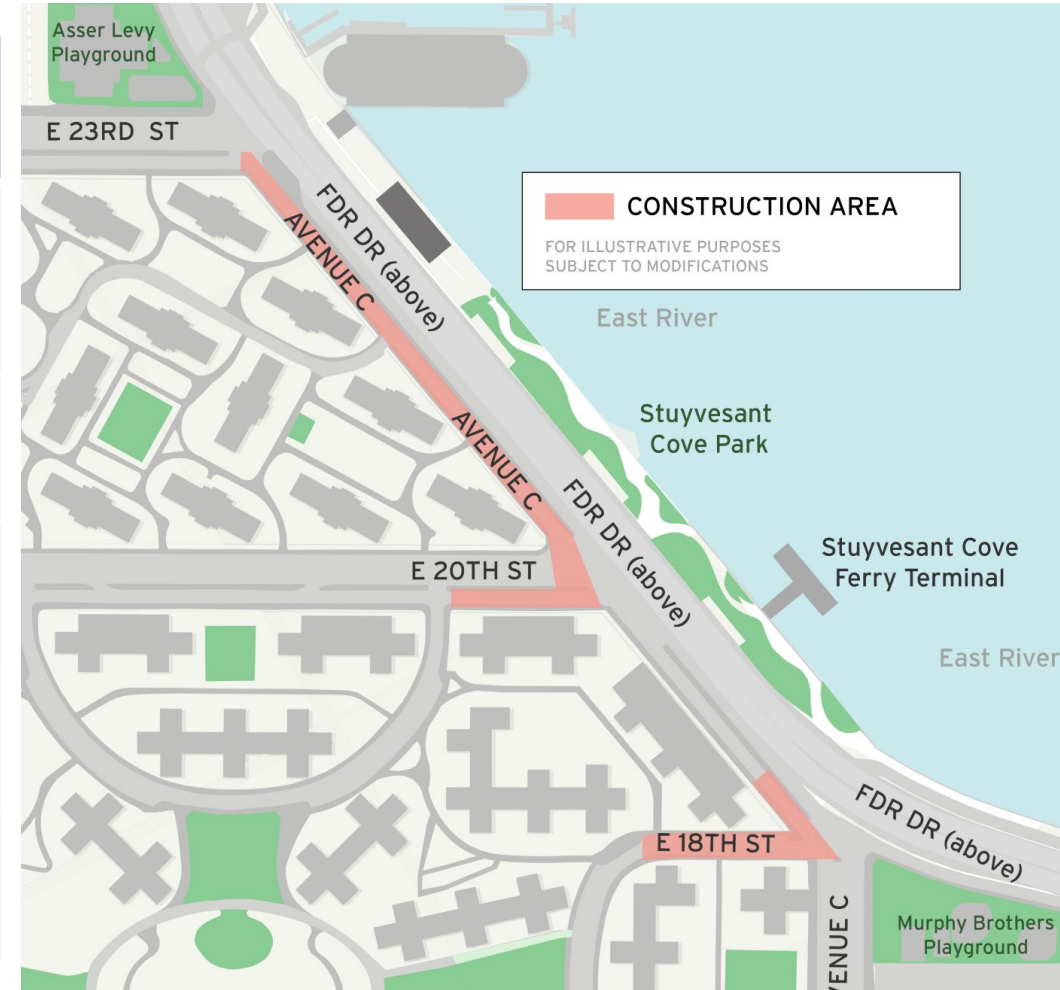

PC | Construction Photos



Final restoration at Delancey Street South and Lewis Street – August 2026

PC | Construction Photos



Catch basin installation in Delancey Street North – August 2026



Water main installation in Delancey Street North – August 2026

PC | Construction Photos



PC sewer installation in Columbia Street – August 2026



Gas main installation near E. 20th Street – August 2026

**PROJECT
INFORMATION
DELIVERY**

Upcoming Meetings & Community Events

NYCHA Riis Family Day	Saturday, August 29
NYCHA Vladeck Family Day	Saturday, August 29
Riis TA Meeting	Tuesday, September 8 at 6:00pm
Virtual Riis ESCR Update	Thursday, September 10 at 11:00am
CB3 Parks Meeting	Thursday, September 17 at 6:30pm
CAG Meeting #73	Thursday, September 24 at 6:30pm





QUESTIONS?
